

# RECLAMATION

*Managing Water in the West*

**MP CONSTRUCTION OFFICE**

**Willows, California**

**Construction Progress Report L-29**

**August 2014**



Red Bluff Diversion Dam Decommissioning  
An Excavator breaking apart concrete block.



U.S. Department of the Interior  
Bureau of Reclamation  
Mid-Pacific Region



CONSTRUCTION PROGRESS REPORT (L-29)  
 MP CONSTRUCTION OFFICE  
 MID-PACIFIC REGION  
 AUGUST 2014

CONTENTS

	PAGE
LOCATION MAP.....	i
STAFFING.....	ii
GLOSSARY OF TERMS.....	iii

<u>CONTRACT/SPECS OR P.O. NO., CONTRACTOR, AND CONTRACT NAME</u>	<u>PAGE</u>	<u>MAP</u>	
	<u>NO.</u>	<u>NO.</u>	
<b>CCAO</b>	<b>1</b>		
R10PC20R15 20-C0649A Abide International, Inc. Fixed Wheel Gate Rehabilitation – Folsom Unit, American River Division, Central Valley Project, California	3		1
R10PC20019 20-C0689 Andritz Hydro Corp. Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement – Folsom Unit, American River Division, Central Valley Project, California	4		1
R10PC20767 20-C0703 Voith Siemens Hydro Power Generation, Inc. Folsom Power Plant U1, U2, and U3 Replacement Runners – Folsom Unit, American River Division, Central Valley Project, California	5		1
R10PC20114 20-C0754 Shimmick Construction Co., Inc. Folsom Dam – Safety of Dams Modification – MIAD Key-Block – Folsom Unit, American River Division, Central Valley Project, California	6		1
R13PC20211 20-C0798 B.C Schmidt Construction, Inc. New Melones Artifact Storage Building – New Melones Unit, East Side Division, Central Valley Project, California	7		2
R13PC20092 20-C0807 Suulutaaq, Inc. Mormon Island Auxiliary Dam Overlay – Folsom Unit, American River Division, Central Valley Project, California	9		1
R13PC20159 None GD Nielson Construction, Inc. Lake Berryessa Concessions Area Improvements – Lake Berryessa, Solano Project, California	12		4
<b>KBAO</b>	<b>15</b>		
<b>LBAO</b>	<b>19</b>		
R12PC20137 20-C0796 Algerine West Construction, Inc. Prosper Creek Dam OHV Bridge Crossing – Stampede Division, Washoe Project, California	21		5



R13PC20088	20-C0808	Knight Construction and Supply, Inc.	22	5
Prosser Creek Dam Refurbish High-Pressure Gate Seats and Regulating Gates – Stampede Division, Washoe Project, California				
R14PC00083	20-C0823	Site Work Solutions, Inc	23	5
Marble Bluff Dam, Asphalt Pavement Rehabilitation – Stampede Division, Washoe Project, California				
<b>NCAO</b>			<b>25</b>	
R10PC20102	20-C0755	Andritz Hydro Corp.	27	6
Spring Creek Powerplant Generators G1 and G2 Rewinds – Trinity River Division, Central Valley Project, California				
R13PC20172	No. 20-C0817	California Pavement Maintenance Company	28	6
JF Carr, Spring Creek, and Trinity Powerplants Pavement Rehabilitation Trinity River Division, Central Valley Project, California				
R13PC20169	20-C0820	E.C. Smith, Inc.	30	8
Red Bluff Diversion Dam Decommissioning - Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California				
R10PC20025	None	Tehama Environmental Solutions, Inc.	31	9
Coleman Fish Hatchery Water Intakes Vegetation Replacement and Monitoring – Shasta Division, Central Valley Project, California				
R11PC20235	None	Tehama Environmental Solutions, Inc.	32	8
Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation – Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California				
R14PC00066	None	Alsco Inc.	33	8
Red Bluff Well Enhancement, Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California				
<b>SCCAO</b>			<b>35</b>	
R11PC20185	20-C0778	Contra Costa Electric, Inc.	37	10
Tracy 13.8kV Switchgear/Breaker Replacement – Tracy Pumping Plant and Substation – Delta Division, Central Valley Project, California				
R13PC20508	20-C0788	Slayden Construction Group, Inc.	39	11
San Luis Demonstration Treatment Plant –San Luis Unit, West Stanislaus Division, Central Valley Project, California				
R13PC20105	20-C0813	Valentine Corporation	41	10
Tracy Fish Collecting Facilities, Secondary Louver Replacement – Delta Division, Central Valley Project, California				




<b>Regional</b>	<b>43</b>
R13PC20005 20-C0799 Contractor Services Group, Inc. Baldwin Creek Fish Barrier – Battle Creek Salmon and Steelhead Restoration Project, California	45
R13PC20143 20-C0803 T.L. Peterson, Inc. North Battle Creek Feeder Dam Access Road Completion – Battle Creek Salmon and Steelhead Restoration Project, California	46
<b>Contracts in Warranty Status</b>	<b>47</b>
R09PC20R03 20-C0677 Transformer K1A and K2A Replacements, Folsom Power Plant	49
R10PC20R11 20-C0730 Red Bluff Pumping Plant and Fish Screen, Pumps and Motors	49
R10PC20R80 20-C0759 Drought Relief–Construction of New Wells	49
R12PC20062 20-C0785 Tracy Fish Collection Facility - Trash Rake Monorail Extension	49
R13PC20194 20-C0800 Tracy Fish Collection Facility – Pavement Rehabilitation	49
R13PC20507 20-C0792 North Fork Pipeline Repair	49
R13PC20512 20-C0800 Tracy Facility - Pavement Rehabilitation	49



# Mid-Pacific Region

**RECLAMATION**  
Managing Water in the West

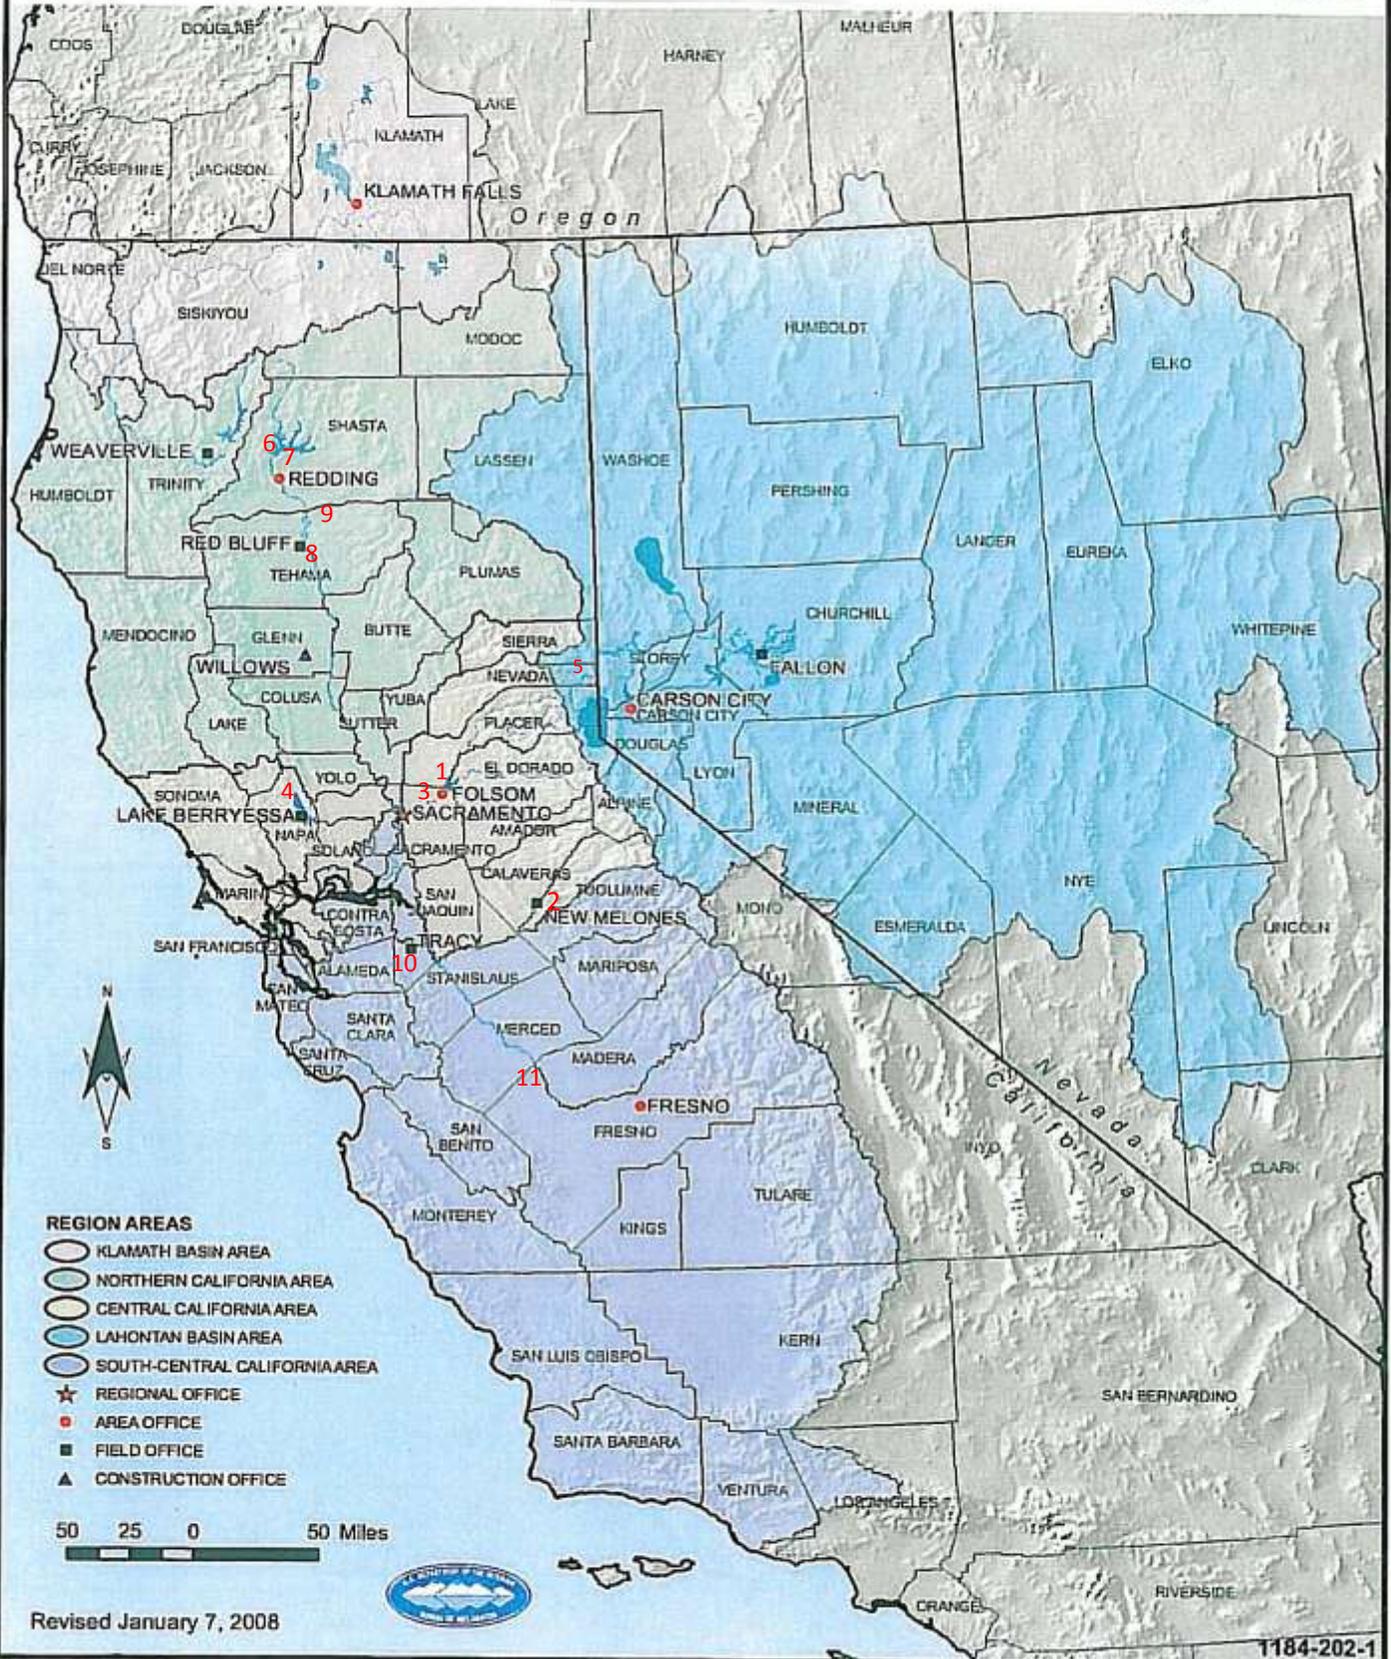



**STAFFING – MID PACIFIC CONSTRUCTION OFFICE**

The Mid Pacific Construction Office had 48 construction and administrative employees at the close of this month as follows:

Construction Engineer's Office	2
Preaward & Project Management Group	3
Administrative Management	7
Division of Field Engineering	21
Division of Office Engineering	8
Materials Lab Branch	7



## **GLOSSARY OF ACRONYMS AND ABBREVIATIONS**

### **MEANING**

CCAO	Central California Area Office
CVP	Central Valley Project
KBAO	Klamath Basin Area Office
LBAO	Lahontan Basin Area Office
MP	Mid Pacific Regional Office
MPCO	Mid-Pacific Construction Office
NCAO	Northern California Area Office
SCCAO	South Central California Area Office
TO	Tracy Office



CCAO



Contract No. R10PC20R15  
Specification No. 20-C0649A  
Fixed Wheel Gate Rehabilitation – Folsom Unit, American River Division, Central Valley  
Project, California  
Abide International, Inc., Sonoma, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	85.9%
Contractor Earnings:	August	\$0
	Previous	\$7,989,508.17
	Total to Date	\$7,989,508.17

Area Office Project Management  
Project Manager: Jesse Castro, CC-607

Office Engineering  
Contract Administrator: Larry Bowman, MPCO-240

No invoices were received this period.

A modification to definitize all previous modifications and resolve uncompleted work is being completed.

Field Engineering  
Construction Manager: Henry Garcia, MPCO-310  
Construction Representative: Gustavo Aguilera, MPCO-337; Bill Linder, MPCO-312; Howard Diedrich, MPCO-316

Number of Contract Employees: 0

Work Performed:  
No site work was performed this period. The contractor did not complete the contract site work, and will perform no further site work.

Contract No. R10PC20019

Specification No. 20-C0689

Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement –

Folsom Unit, American River Division, Central Valley Project, California

Andritz Hydro Corp, Charlotte, NC

Work Performed:	August	0%
	Time Elapsed	89.5%
	Work Completed	76.8%

Contractor Earnings:	August	\$0
	Previous	\$15,685,567.71
	Total to Date	\$15,685,567.71

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Casey Arthur, MPCO-245

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Todd Dooley, MPCO-314

Number of Contract Employees: 0

Work performed:

No work was performed this period. Work is scheduled to restart in October 2014.

Contract No. R10PC20767

Specification No. 20-C0703

Folsom Power Plant U1, U2, and U3 Replacement Runners – Folsom Unit, American River

Division, Central Valley Project, California

Voith Siemens Hydro Power Generation, Inc., York, PA

Work Performed:	August	0%
	Time Elapsed	88.2%
	Work Completed	73.7%
Contractor Earnings:	August	\$0
	Previous	\$5,488,977.80
	Total to Date	\$5,488,977.80

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Casey Arthur, MPCO-245

No invoices were received this period.

Field Engineering

Construction Manager: N/A supply contract

Construction Representative: N/A supply contract

Number of Contract Employees: N/A supply contract

Work performed: N/A supply contract

Contract No. R10PC20114  
Specification No. 20-C0754  
Folsom Dam – Safety of Dams Modification – MIAD Key-Block – Folsom Unit, American  
River Division, Central Valley Project, California.  
Shimmick Construction Co., Inc., Sacramento, CA

Work Performed:	August	2.4%
	Time Elapsed	100%
	Work Completed	100%
Contractor Earnings:	August	\$1,061,140.93
	Previous	\$44,006,112.97
	Total to Date	\$45,067,253.90

Area Office Project Management  
Project Manager: Larry Hobbs, CC-106

Office Engineering  
Contract Administrator: Larry Bowman, MPCO-240

Final invoice number 36-Final was received this period.

Office Engineering resolved the request for equitable adjustment for encountering harder than expected bedrock.

Field Engineering  
Construction Manager: Henry Garcia, MPCO-310  
Construction Representative: Howard Diedrich, MPCO-316; Sean Frische, MPCO-317

Number of Contract Employees: 0

Work Performed:  
No site work was performed as all site work was completed in February 2013. The substantial completion date was January 4, 2013.

Contract No. R13PC20211

Specification No. 20-C0798

New Melones Artifact Storage Building – New Melones Unit, East Side Division, Central Valley Project, California

B. C. Schmidt Construction, Inc., Williams, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	95.2%
Contractor Earnings:	August	\$0.00
	Previous	\$1,419,965.53
	Total to Date	\$1,419,965.53

Area Office Project Management

Project Manager: Laureen Perry, MP-153

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

No invoice was received during this period.

The Substantial Completion letter was issued to the contractor on June 9, 2014. The project was substantially complete on April 29, 2014. The Warranty of Construction extends until April 28, 2015.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Dennis Schuenemann, MPCO-338

Number of Contract Employees: 4

Work Performed:

B.C. Schmidt performed the following work:

- The contractor continued to complete punch list item work
- A manufacturer's representative was onsite to replace the OMNTEC alarm/reset box. Once installed, the alarms were tested and confirmed to be operational.
- The contractor repaired the seal to the entry door to the office building.
- Videos for the HVAC O&M, Fire Sprinkler System, Fire Alarm and Security Systems training were prepared by the contractor.

J.H. Simpson performed the following work:

- An HVAC Technician was onsite to create the O&M video with the contractor.
- All fan belts and HVAC components were inspected by the technician. Once all components were secured and one fan belt was replaced, the system was confirmed to be operational.

Door28, Inc. performed the following work:

- A door representative was onsite again to gather more information for their plan to resolve the issues with the two non-compliant steel doors and frames.



New Melones Artifact Storage Building  
A new reset/alarm box for the Sanitary Sewage Holding Tank was mounted to the office wall and all wires connected and tested.

Contract No. R13PC20092

Specification No. 20-C0807

Mormon Island Auxiliary Dam Overlay – Folsom Unit, American River Division, Central Valley Project, California

Suulutaaq, Inc., Suisun City, CA

Work Performed:	August	0%
	Time Elapsed	41.1%
	Work Completed	20.0%

Contractor Earnings:	August	\$2,277,267.79
	Previous	\$6,940,670.37
	Total to Date	\$9,217,938.16

Area Office Project Management

Project Manager: Kyle Keer, CC-108

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

Invoice 10 was received and forwarded to the Denver finance office for processing. It was not for work done this period, but for work through July 20, 2014.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Sean Frische, MPCO-317 Zahid Wazid, MPCO-349, Gustavo Aguilera, MPCO-337, Arnold Moseby, MPCO-327, Bill Linder, MPCO-212, Dennis Schuenemann, MPCO-338

Number of Contract Employees: 41

Work Performed:

Embankment Backfill Activities:

Granite Construction performed the following work:

- Completed placing and compacting about ninety percent of the 2-foot thick bottom layer of the fine filter blanket drain between stations 434+00 and 445+00.
- Completed placing and compacting ninety percent of the 4-foot thick coarse filter blanket drain between stations 434+00 and 454+00.
- Completed ninety percent of the 1-foot thick fine filter blanket cover.
- Started placing Zone B material over the finished blanket drain fine filter between stations 434+00 and 454+00, completing a 16-inch.
- Continued placing the filter chimney sections and the Zone A and Zone B embankments between stations 416+00 and 430+00.
- Started placing the cobble slope protection on the final embankment slope between stations 416+00 and 430+00.

**Commercial Material:**

Granite Construction continued hauling in commercial sand from the Newman and Teichert plants, and coarse filter from the Bradshaw plant.

**Toe Drain Activities:**

Granite Construction completed the final backfill of the Type A toe drain between stations 430+00 and 443+00 after Suulutaaq installed the 24-inch perforated high density polyethylene pipe (HDPE).

Suulutaaq finished installing the 24-inch perforated pipe between stations 448+55 and 442+49 and Granite completed placing and compacting the coarse filter backfill around the pipe for Segment 5 of the toe drain.

Suulutaaq installed single weir box at Outfall 5 and conducted initial video inspection of the installed HDPE pipes.

**Stockpile Processing Activities:**

Fisher Industries resumed operation at the primary processing plant to produce 1 1/4-inch minus material, Zone A material, and Zone B material.

Fisher Industries continued processing and washing fine and coarse filter materials at the wash-plant. The onsite-processed fine filter was blended with commercial sand at a 50:50 ratio to produce filter material for the critical chimney zones. The onsite-processed sand was used at the downstream chimney sections.

Kiewit continued hauling material from JFP Phase 4 site to MIAD, with 150,170-cyds hauled to date.

**Instrumentation:**

Suulutaaq, Inc. extended the six-inch pipe casing at the key-block.

**Water Pollution Control/ Stormwater Pollution Prevention Plan (SWPPP):**

Suulutaaq continued installing best management practices in preparation for the rainy season.



Mormon Island Auxiliary Dam Overlay  
The contractor installing 24" perforated HDPE pipe

Contract No. R13PC20159

Specification No. None

Lake Berryessa Concessions Area Improvements - Lake Berryessa - Solano Project, California

G.D. Nielson Construction, Inc. Napa, CA

Work Performed:	August	36.4%
	Time Elapsed	98.9%
	Work Completed	65.4%
Contractor Earnings:	August	\$258,454.80
	Previous	\$342,740.20
	Total to Date	\$601,195.00

Area Office Project Management

Project Manager: Pete Funkhouser, CCAO

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

Invoice 3 was received in the month of August.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Bill Linder, MPCO-312

Number of Contract Employees: 21

Work Performed:

The contractor began onsite work on June 2, 2014. Contractor is working on RV dump Stations and water distribution systems. Contract completion date remains September 3, 2014.



Lake Berryessa Concessions Area Improvements  
Installation of Water Distribution Systems



**KBAO**



There were no active construction projects underway for the Klamath Basin Area Office in August 2014.



**LBAO**



Contract No. R12PC20137

Specification No. 20-C0796

Prosser Creek Dam OHV Bridge Crossing – Stampede Division, Washoe Project, California

Algerine West Construction, Inc., Jamestown, CA

Work Performed	August	0%
	Time Elapsed	100%
	Work Completed	64.2%

Contractor Earnings	August	\$0
	Previous	\$102,335.00
	Total to Date	\$102,335.00

Area Office Project Management

Project Manager: Locke Hahne, LO-400

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

No invoices were received this period.

The remaining office work for the contractor to perform is to provide as-built drawings, which will be done after the repairs described below are made.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Dennis Schuenemann, MPCO-338

Number of Contract Employees: 0

Worked Performed:

No site work was performed this period. The work remaining for the contractor to perform is repair of the damaged endwalls, and replacement of two damaged braces.

Contract No. R13PC20088  
Specification No. 20-C0808  
Prosser Creek Dam Refurbish High-Pressure Gate Seats and Regulating Gates – Stampede  
Division, Washoe Project, California  
Knight Construction and Supply, Inc., Deer Park, WA

Work Performed	August	0%
	Time Elapsed	41.6%
	Work Completed	1.3%
Contractor Earnings	August	\$0
	Previous	\$27,776.00
	Total to Date	\$27,776.00

Area Office Project Management  
Project Manager: Locke Hahne, LO-400

Office Engineering  
Contract Administrator: Ryan Hennigan, MPCO-211

No invoices were received this period.

Field Engineering  
Construction Manager: Henry Garcia, MPCO-310  
Construction Representative: Todd Dooley, MPCO-314

Number of Contract Employees: 0

Worked Performed:  
Site work has not begun. It is scheduled to begin in September 2014.

Contract No. R14PC00083

Specification No. 20-C0823

Marble Bluff Dam, Asphalt Pavement Rehabilitation – Stampede Division, Washoe Project,  
California

Site Work Solutions, Inc, Redding CA

Work Performed	August	0%
	Time Elapsed	0%
	Work Completed	0%
Contractor Earnings	August	\$0.00
	Previous	\$0.00
	Total to Date	\$0.00

Area Office Project Management

Project Manager: Scott Schoenfeld, LO-410

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

No invoices were received this period.

The contract was awarded during this period

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Michael Manlick, MPCO-313

Number of Contract Employees: 0

Worked Performed:

No onsite work was performed this period. Onsite work will occur after the critical submittals are approved.



NCAO



Contract No. R10PC20102  
Specification No. 20-C0755  
Spring Creek Powerplant Generators G1 and G2 Rewinds – Trinity River Division, Central Valley Project, California  
Andritz Hydro Corp., Charlotte, NC

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	69.9%
Contractor Earnings:	August	\$0
	Previous	\$7,923,921.77
	Total to Date	\$7,923,921.77

Area Office Project Management  
Project Manager: Joe Ascoli, NC-650

Office Engineering  
Contract Administrator: Kevin Jacobs, MPCO-214

No invoices were received this period.

Field Engineering  
Construction Manager: Steve Holmes, MPCO-320  
Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:  
No site work was performed this period. The restart of site work is scheduled to occur on November 2, 2014.

Contract No. R13PC20172

Specification No. 20-C0817

JF Carr, Spring Creek, and Trinity Powerplant Pavement Rehabilitation – Trinity River Division,  
Central Valley Project, California

California Pavement Maintenance Company, Inc., Sacramento, CA

Work Performed	August	0.0%
	Time Elapsed	85.8%
	Work Completed	0.0%
Contractor Earnings	August	\$0.00
	Previous	\$ 0.00
	Total to Date	\$ 0.00

Area Office Project Management

Project Manager: Hank Harrington, NCAO-210

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

No invoice was received this period.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Fernando Pavone, MPCO-333

Number of Contract Employees: 6

Work performed:

The contractor began work this period which included crack sealing and asphalt repair at J.F. Carr Powerplant.



JF Carr, Spring Creek, and Trinity Powerplant Pavement Rehabilitation  
California Pavement Maintenance Company, Inc. Contractor doing asphalt repairs

Contract No. R13PC20169

Specification No. 20-C0820

Red Bluff Diversion Dam Decommissioning – Sacramento Canals Unit, Sacramento River

Division, Central Valley Project, California

E.C. Smith, Inc., Anderson, CA

Work Performed:	August	6.4%
	Time Elapsed	60.8%
	Work Completed	65.7%
Contractor Earnings:	August	\$211,640.00
	Previous	\$1,945,900.00
	Total to Date	\$2,157,540.00

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Manager: Kevin Jacobs, MPCO-214

Invoice 5 was received on August 27, 2014, and forwarded to the Denver finance office for processing. It was for work performed between August 1, 2013 and August 30, 2014.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Jeff Kelly, MPCO-361

Number of Contract Employees: 15

Work Performed:

- The motor mounts for the Archimedes screw pumps were removed. The upper portion of the concrete blocks supporting them was demolished to below finish grade of the backfill.
- Operators finished backfilling the Research Pumping Plant.

Contract No. R10PC20025

Specification No. None

Coleman Fish Hatchery Water Intakes Vegetation Replacement and Monitoring – Shasta

Division, Central Valley Project, California

Tehama Environmental Solutions, Inc., Red Bluff, CA

Work Performed:	August	0%
	Time Elapsed	67.1%
	Work Completed	92.8%
Contractor Earnings:	August	\$0
	Previous	\$656,891.52
	Total to Date	\$656,891.52

Area Office Project Management

Project Manager: Hank Harrington, NC-210

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

No invoices were received this period.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Fernando Pavone, MPCO-333

Number of Contract Employees: 0

Work performed:

The contractor's current activity consists of maintaining vegetation it planted in 2010.

Contract No. R11PC20235

Specification No. None

Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation –  
Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California  
Tehama Environmental Solutions, Inc., Red Bluff, CA

Work Performed:	August	1.4%
	Time Elapsed	42.2%
	Work Completed	93.4%

Contractor Earnings:	August	\$57,810.52
	Previous	\$4,435,040.08
	Total to Date	\$4,492,850.60

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

Invoice 13 was received in August.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: David Derk, MPCO-334

Number of Contract Employees: 0

Work performed:

The contractor performed no work this period, but plans to return soon to perform weeding.

Contract No. R14PC00066

Specification No. None

Red Bluff Well Enhancement – Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California

AlSCO, Inc., Red Bluff, CA

Work Performed:	August	0%
	Time Elapsed	0%
	Work Completed	0%
Contractor Earnings:	August	\$0
	Previous	\$0
	Total to Date	\$0

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

No invoices were received this period.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Jeff Kelly, MPCO-361

Number of Contract Employees: 0

Work performed:

The contract was awarded July 16, 2014, and the contractor anticipates work to begin in September 2014.



SCCAO



Contract No. R11PC20185

Specification No. 20-C0778

Tracy 13.8kV Switchgear/Breaker Replacement – Tracy Pumping Plant and Substation – Delta

Division, Central Valley Project, California

Contra Costa Electric Corp., Martinez, CA

Work Performed:	August	7.0%
	Time Elapsed	76.8%
	Work Completed	27.1%

Contractor Earnings:	August	\$943,661.30
	Previous	\$2,696,252.78
	Total to Date	\$3,639,914.08

Area Office Project Management

Project Manager: Warren Feng, TO-438

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

This is a design/build contract.

An invoice in the amount of \$943,661.30 was forwarded to the Denver office for processing.

A modification was executed during this period to fully fund the contract.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: David Derk, MP-334

Number of Contract Employees: 4

Work Performed:

Contra Costa Electric, Inc. performed the following work:

- The 125v DC battery rack and batteries were installed, along with the jumper busses between each battery. The assembly of 125v DC panel BCC was completed.
- Conduit was installed between the 125v DC battery rack and the 125v DC panel BCB in the basement of the control building.
- Conductors were tested between the 125v DC panels MCA, BCB, and BCC.
- Two 20 amp breakers were replaced in panel MCA with 70 amp breakers for the two new 125v DC battery chargers.
- Two runs of control conductors between building 11A and the Jones Pumping Plant were pulled.



Tracy 13.8kV Switchgear / Breaker Replacement (RAX 472)  
125v DC batteries assembled with clear plastic safety shield

Contract No. R13PC20508  
Specification No. 20-C0788  
San Luis Demonstration Treatment Plant – San Luis Unit, West San Joaquin Division, Central Valley Project, California  
Slayden Construction Group, Inc., Stayton, OR

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	94.33%
Contractor Earnings:	August	\$78,009.46
	Previous	\$21,636,837.76
	Total to Date	\$21,714,847.22

Area Office Project Management  
Project Manager: Cheryl Carter, SCC-105

Office Engineering  
Contract Administrator: Cassandra Arthur, MPCO-245

Invoice No. 20 was received and forwarded to Denver finance office for processing. It was not for work done this period, but for work through July 31, 2014.

No modifications were executed during this time period.

Field Engineering  
Project Engineer: Chris Van Deusen, MPCO-345

Number of Contract Employees: 6

Work performed:  
The 30-day performance period, which began on July 22, 2014, continued.

Slayden Construction performed the following work:

- Installation of permanent equipment identification tags.
- Troubleshooting equipment issues.
- Demobilization efforts and punch list items.
- Coordinating with manufacturer's representatives and operators, as necessary.
- Miscellaneous site cleanup and housekeeping activities.

Water Dynamics continued to operate and maintain treatment systems, troubleshoot equipment issues, and take water samples for analysis.

Mason Painting continued touch up painting throughout the building.



San Luis Demonstration Treatment Plant  
Contractor checking backwash pump discharge piping

Contract No. R13PC20105  
Specification No. 20-C0813  
Tracy Fish Collecting Facilities, Secondary Louver Replacement – Delta Division, Central Valley Project, California  
Valentine Corporation, San Rafael, CA

Work Performed	August	0.0%
	Time Elapsed	84.0%
	Work Completed	92.3%
Contractor Earnings	August	\$0.00
	Previous	\$4,052,139.24
	Total to Date	\$4,052,139.24

Area Office Project Management  
Project Manager: Warren Feng, TO-438

Office Engineering  
Contract Administrator: Larry Bowman, MPCO-240

No invoice was received this reporting period.

Field Engineering  
Construction Manager: Randy Wyatt, MPCO-305  
Construction Representative: Fernando Pavone, MPCO-333

Number of Contractor Employees: 7  
Number of Subcontractor Employees: 6

Safety:  
During this period the Valentine Corporation crew conducted daily tool box safety meetings. No safety infractions were observed during this period.

Environmental:  
Valentine Corporation maintained the environmental controls with no issues to report during this period.

Weather:  
The weather during this period was clear and sunny with no rain. The temperature was between 56° and 105° and 0.00” of precipitation.

Work Performed:

Punch List Items:

VC and subcontractor Intralox crew worked on punch list items fixing the items listed, and fixing problems with the fish screens. The crew conducted visual investigation on the screen to determine the problem with the screen rods walking out. Intralox has proposed to provide new screen belting to see if this resolves the problem.



# Regional



Contract No. R13PC20005

Specification No. 20-C0799

Baldwin Creek Fish Barrier – Battle Creek Salmon and Steelhead Restoration Project, California  
Contractor Services Group, Inc.

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	100%

Contractor Earnings:	August	\$0.00
	Previous	\$3,522,425.40
	Total to Date	\$3,522,425.40

Area Office Project Management

Project Manager: Mary Marshall, MP-203

Office Engineering

Contract Administrator: Kent Perkes, MPCO-225

Final contract modification executed on July 22, 2014.

Final Payment submitted August 6, 2014, but has been rejected from FBMS.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: John Pospishil, MPCO-321

Construction Inspector: Jason Foust, MPCO-325, and Jeff Kelly, MPCO-361

Number of Contract Employees: 0

Work Performed:

No Field work was performed this period. Substantial completion was issued March 6, 2014.

The one year warranty period will expire March 5, 2015.

Contract No. R13PC20143

Specification No. 20-C0803

North Battle Creek Feeder Dam Access Road Completion - Battle Creek Salmon and Steelhead  
Restoration Project, California

T. L. Peterson, Inc., Red Bluff, CA

Work Performed:	August	1%
	Time Elapsed	100%
	Work Completed	95%
Contractor Earnings:	August	\$0.00
	Previous	\$266,711.00
	Total to Date	\$266,711.00

Area Office Project Management

Project Manager: Mary Marshall, MP-203

Office Engineering

Contract Administrator: Kent Perkes, MPCO-225

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: John Pospishil, MPCO-321

Field Inspectors: John Pospishil, MPCO-321

Number of Contract Employees: 5

Work performed:

Rock Stabilization Anchor Pull Testing:

Subcontractor Neil's controlled blasting was onsite to perform pull-out testing on the anchors for the rock block stabilization and rock slope stabilization. An engineer from Holdrege and Kull was onsite to witness the testing. Results of three tests, performed at locations determined by the engineer, were provided to Reclamation.

# Contracts in Warranty Status



R09PC20R03 20-C0677 Transformer K1A and K2A Replacements, Folsom Power Plant

There was no Office Engineering Administrative activity this period.

5-year warranty for K1A extends to January 30, 2016, and that for K2A extends to January 4, 2017.

R10PC20R11 20-C0730 Red Bluff Pumping Plant and Fish Screen, Pumps and Motors

There was no Office Engineering Administrative activity this period.

3-year warranty extends to August 2015.

R10PC20R80 20-C0759 Drought Relief-Construction of New Wells

There was no Office Engineering Administrative activity this period.

1-year warranty extends to August 7, 2014.

R12PC20062 20-C0785 Tracy Fish Collection Facility - Trash Rake Monorail Extension

There was no Office Engineering Administrative activity this period.

1-year warranty extended to April 24, 2014.

R13PC20194 20-C0800 Tracy Fish Pavement Rehabilitation

There was no Office Engineering Administrative activity this period.

1-year warranty extends to October 22, 2014.

R13PC20507 20-C0792 North Fork Pipeline Repair

There was no Office Engineering Administrative activity this period.

1-year warranty extends to November 11, 2014.

R13PC20512 20-C0800 Tracy Facility Pavement Rehabilitation

There was no Office Engineering Administrative activity this period.

1-year warranty extends to October 22, 2014.
