

RECLAMATION

Managing Water in the West

MP CONSTRUCTION OFFICE

Willows, California

Construction Progress Report L-29

August 2013



Baldwin Creek Fish Barrier
Barrier structure in early stage of construction



U.S. Department of the Interior
Bureau of Reclamation
Mid-Pacific Region

CONSTRUCTION PROGRESS REPORT (L-29)
MP CONSTRUCTION OFFICE
MID-PACIFIC REGION
August 2013

CONTENTS

	PAGE
LOCATION MAP.....	i
STAFFING.....	ii
GLOSSARY OF TERMS.....	iii


<u>CONTRACT/SPECS OR P.O. NO., CONTRACTOR, AND CONTRACT NAME</u>	PAGE	MAP
	<u>NO.</u>	<u>NO.</u>
CCAO	1	
R10PC20R15 20-C0649A Abide International, Inc. Fixed Wheel Gate Rehabilitation – Folsom Unit, American River Division, Central Valley Project, California	3	1
R10PC20019 20-C0689 Andritz Hydro Corp. Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement – Folsom Unit, American River Division, Central Valley Project, California	4	1
R10PC20767 20-C0703 Voith Siemens Hydro Power Generation, Inc. Folsom Power Plant U1, U2, and U3 Replacement Runners – Folsom Unit, American River Division, Central Valley Project, California	6	1
R10PC20114 20-C0754 Shimmick Construction Co., Inc. Folsom Dam – Safety of Dams Modification – MIAD Key-Block – Folsom Unit, American River Division, Central Valley Project, California	7	1
R10PC20R57 20-C0760 Building Solutions, Inc. Folsom Dam Civil Maintenance Building – Folsom Unit, American River Division, Central Valley Project, California	8	1
R12PC20104 20-C0792 Anderson-Burton Construction Northfork Pipeline Repair - Folsom Pumping Plant – Folsom Unit, American River Division, Central Valley Project, California	10	1
R13PC20211 20-C0798 B.C Schmidt Construction, Inc. New Melones Artifact Storage Building – New Melones Unit, East Side Division, Central Valley Project, California	11	2
R13PC20084 20-C0805 Collins Electrical Company, Inc. Nimbus Powerplant Transformer Anchorage System – Folsom Unit, American River Division, Central Valley Project, California	12	3
R13PC20092 20-C0807 Suulutaq, Inc. Mormon Dam Auxiliary Dam Overlay – Folsom Unit, American River Division, Central Valley Project, California	13	1

R10PC20859	None	Trofholz Technologies, Inc.	14	1
Folsom Dam and Powerplant Site Security System – Folsom Unit, American River Division, Central Valley Project, California				
KBAO			15	
LBAO			19	
R12PC20137	20-C0796	Algerine West Construction, Inc.	21	4
Prosser Creek Dam OHV Bridge Crossing – Stampede Division, Washoe Project, California				
NCAO			23	
R10PC20744	20-C0712	National Electric Coil, Inc.	25	5
J.F. Carr Power Plant, Generator G1 and G2 Rewinds – Trinity River Division, Central Valley Project California				
R10PC20102	20-C0755	Andritz Hydro Corp.	26	5
Spring Creek Powerplant Generators G1 and G2 Rewinds – Trinity River Division, Central Valley Project, California				
R12PC20044	20-C0774a	Eaton Corp.	27	5, 6
Station Service Switchgear Replacement – Trinity River Division, Central Valley Project, California				
R12PC20053	20-C0789	Ray-Mac Mechanical, Inc.	28	6
Shasta Powerplant Control and Computer Room HVAC Replacement – Shasta Division, Central Valley Project, California				
R10PC20025	None	Tehama Environmental Solutions, Inc.	29	7
Coleman Fish Hatchery Water Intakes Vegetation Replacement and Monitoring – Shasta Division, Central Valley Project, California				
R11PC20235	None	Tehama Environmental Solutions, Inc.	30	8
Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation – Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California				
SCCAO			31	
R11PC20185	20-C0778	Contra Costa Electric Corp.	33	9
Tracy 13.8kV Switchgear/Breaker Replacement – Tracy Pumping Plant and Substation – Delta Division, Central Valley Project, California				
R12PC20062	20-C0785	Monterey Mechanical Co.	34	9
Tracy Fish Collection Facility – Trash Rake Monorail Extension – Delta Division Central Valley Project, California				
R11PC20107	20-C0788	Slayden Construction Group, Inc.	35	10

San Luis Demonstration Treatment Plant – San Luis Unit Drainage – San Luis Unit, West Stanislaus Division, Central Valley Project, California	37	9, 11
R13PC20194 20-C0800 Allright Construction, Inc. Tracy Facility Pavement Rehabilitation – Delta Division, Central Valley Project, California		
Regional	39	
R10PC20R42 20-C0746 RTA Construction/Ray Toney JV Hydropower Facility Modifications-Stage 1 – Battle Creek Salmon and Steelhead Restoration Project, California	41	
R10PC20R80 20-C0759 Layne Christensen Co. Drought Relief–Construction of New Wells–ARRA Project No. 28.002–California	42	
R13PC20005 20-C0799 Contractor’s Services Group, Inc. Baldwin Creek Fish Barrier – Battle Creek Salmon and Steelhead Restoration Project, California	43	
Contracts in Warranty Status	45	
R09PC20R03 20-C0677 Transformer K1A and K2A Replacements, Folsom Power Plant	47	
R10PC20R11 20-C0730 Red Bluff Pumping Plant and Fish Screen, Pumps and Motors	47	
R10PC20R32 20-C0749 Fish Screen Structure Phase 3, Contra Costa Canal	47	
R10PX20R54 20-C0750 Drought Relief, Well Enhancements	47	
R10PC20R33 20-C0752 Red Bluff Pumping Plant and Fish Screens	47	
R10PC20197 20-C0768 Control, Upgrade and Modernization of the Gantry and Bridge Cranes at the Folsom Dam and Powerplant	47	
R12PC20158 20-C0777 Stampede Powerplant and Switchyard Recoatings	47	
R11PC20124 20-C0780 Coleman National Fish Hatchery Barrier Weir Site Modifications	47	
R12PC20193 20-C0791 Shasta Dam Traffic Circle Pavement Rehabilitation	47	

Mid-Pacific Region

RECLAMATION
Managing Water in the West

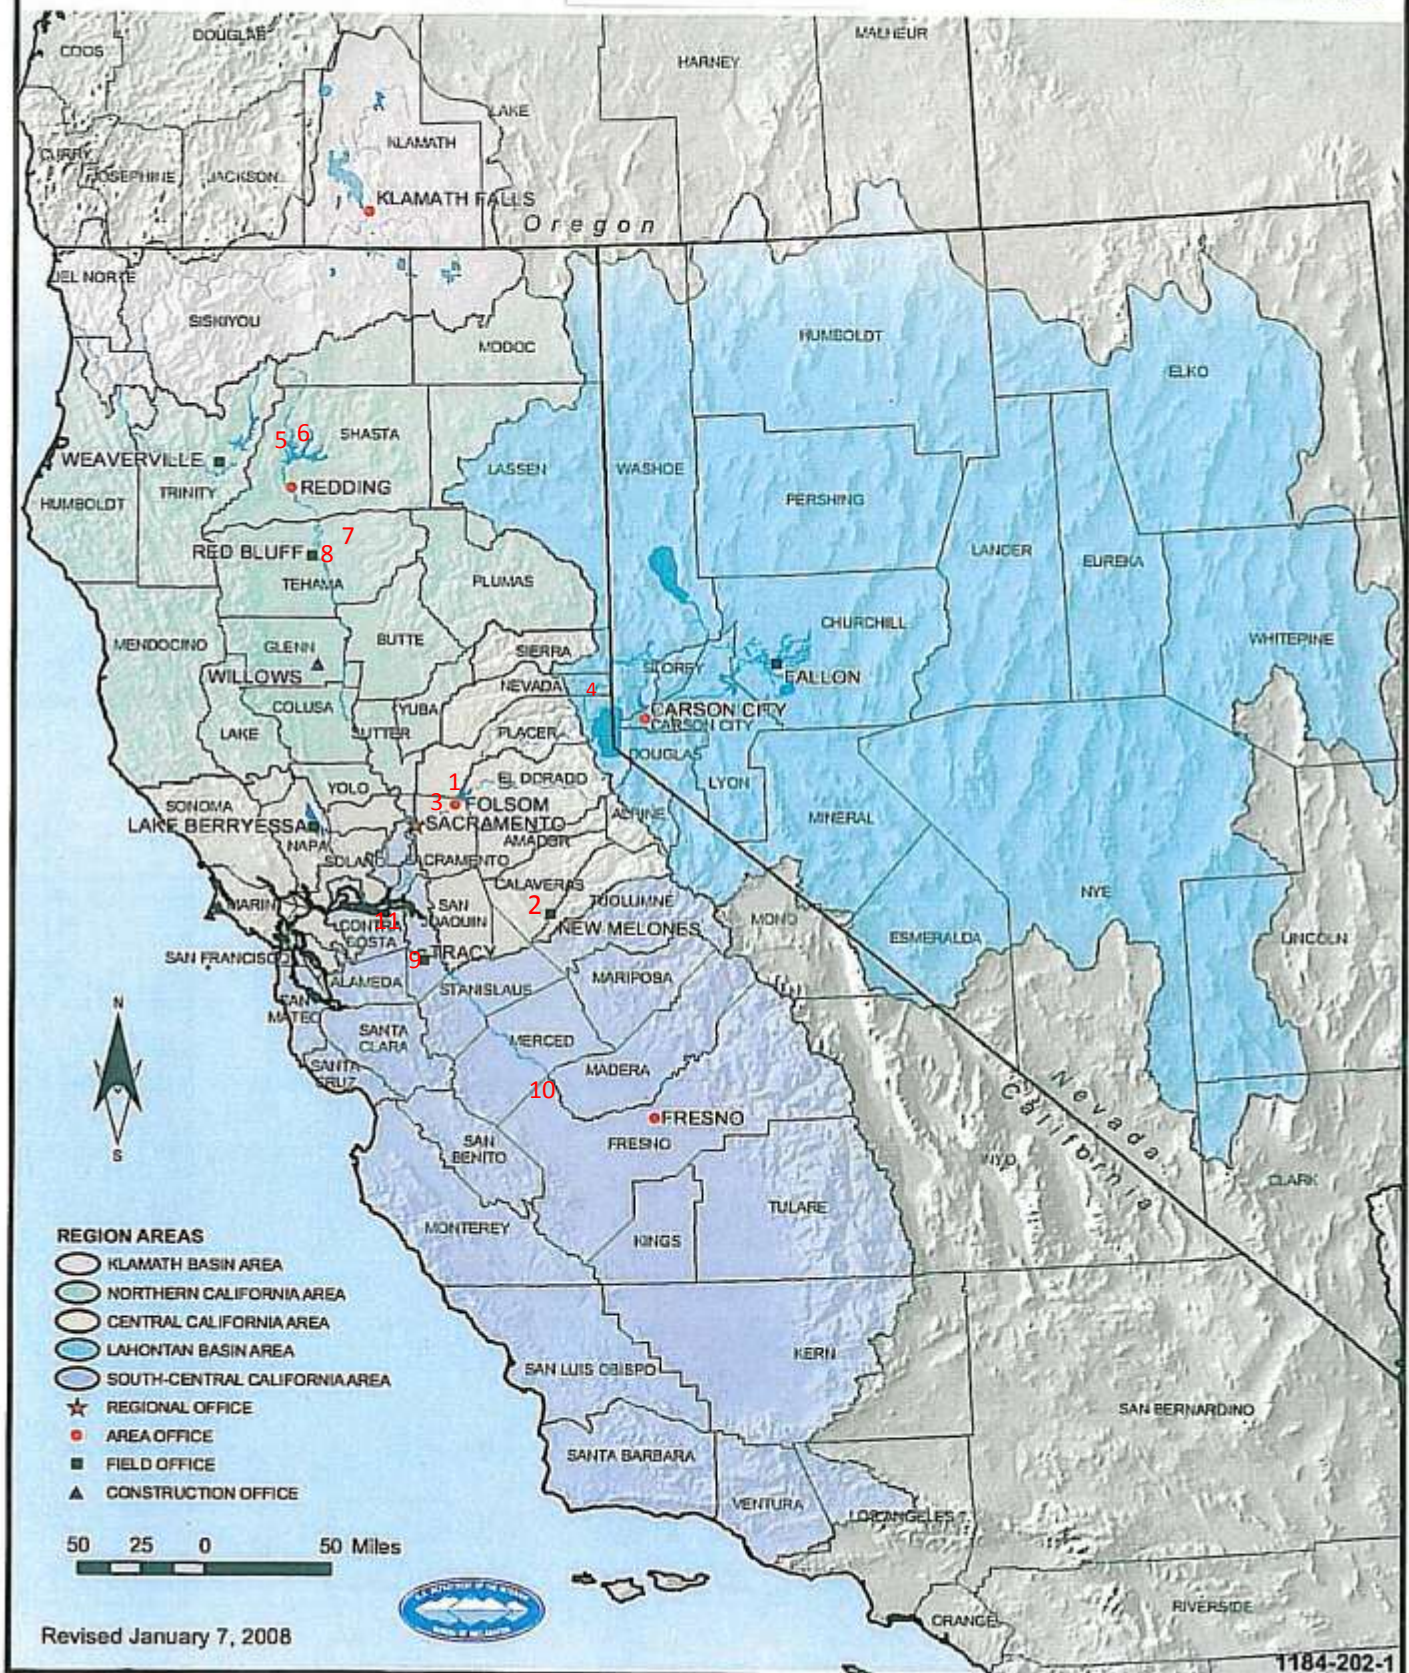

STAFFING – MID PACIFIC CONSTRUCTION OFFICE

The Mid Pacific Construction Office had 59 construction and administrative employees at the close of this month as follows:

Construction Engineer's Office	2
Preaward & Project Management Group	3
Administrative Management	10
Division of Field Engineering	26
Division of Office Engineering	11
Materials Lab Branch	7

GLOSSARY OF ACRONYMS AND ABBREVIATIONS

MEANING

ARRA	American Recovery and Reinvestment Act
CCAO	Central California Area Office
CVP	Central Valley Project
KBAO	Klamath Basin Area Office
LBAO	Lahontan Basin Area Office
MP	Mid Pacific Regional Office
MPCO	Mid-Pacific Construction Office
NCAO	Northern California Area Office
SCCAO	South Central California Area Office
TO	Tracy Office

CCAO

Contract No. R10PC20R15

Specification No. 20-C0649A

Fixed Wheel Gate Rehabilitation – American River Division, Folsom Unit, Central Valley

Project, California

Abide International, Inc., Sonoma, CA

Work Performed:	August	0%
	Time Elapsed	99.1%
	Work Completed	80.5%

Contractor Earnings:	August	\$0
	Previous	\$7,492,283.03
	Total to Date	\$7,492,283.03

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Larry Bowman, MPCO-240

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Gustavo Aguilera, MPCO-337; Bill Linder, MPCO-312; Howard Diedrich, MPCO-316

Number of Contract Employees: 4

Work Performed:

The Contractor performed the work necessary to make Unit 1 operational.

Contract No. R10PC20019

Specification No. 20-C0689

Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement –

Folsom Unit, American River Division, Central Valley Project, California

Andritz Hydro Corp, Charlotte, NC

Work Performed:	August	0%
	Time Elapsed	73.9%
	Work Completed	76.8%

Contractor Earnings:	August	\$0
	Previous	\$15,685,567.71
	Total to Date	\$15,685,567.71

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Madelyn Giles, MPCO-210

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Sergio Vivar, MPCO-311; Todd Dooley, MPCO-314

Number of Contract Employees: 8

Work performed:

The Contractor prepared Exciter No. 1 for commissioning testing and successfully performed the testing (short circuit tests, open circuit saturation tests, excitation tests, and synchronizing tests).



Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement
Andritz Hydro electrician installing boots on the exposed conductors the of Unit 1 Transformer
K1A in preparation for the Open Circuit Saturation Testing

Contract No. R10PC20767

Specification No. 20-C0703

Folsom Power Plant U1, U2, and U3 Replacement Runners – Folsom Unit, American River

Division, Central Valley Project, California

Voith Siemens Hydro Power Generation, Inc., York, PA

Work Performed:	August	0%
	Time Elapsed	92.3%
	Work Completed	74.0%
Contractor Earnings:	August	\$18,095.07
	Previous	\$5,467,717.72
	Total to Date	\$5,485,812.79

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Madelyn Giles, MPCO-210

Invoice 29 was received and forwarded to the Denver finance office for processing. It was not for work done this period, but for work done through July 31, 2013.

Field Engineering

Construction Manager: N/A supply contract

Construction Representative: N/A supply contract

Number of Contract Employees: N/A supply contract

Work performed: N/A supply contract

Contract No. R10PC20114

Specification No. 20-C0754

Folsom Dam – Safety of Dams Modification – MIAD Key-Block – Folsom Unit, American

River Division, Central Valley Project, California.

Shimmick Construction Co., Inc., Sacramento, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	94.9%

Contractor Earnings:	August	\$0
	Previous	\$43,182,626.23
	Total to Date	\$43,182,626.23

Area Office Project Management

Project Manager: Larry Hobbs, CC-106

Office Engineering

Contract Administrator: Larry Bowman, MPCO-240

No invoices were received this period.

All that remains is settling a request for equitable adjustment for encountering harder than expected bedrock.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Howard Diedrich, MPCO-316; Sean Frische, MPCO-317

Number of Contract Employees: 0

Work Performed:

No site work was performed as all site work was complete in February 2013. The substantial completion date was January 4, 2013.

Contract No. R10PC20R57

Specification No. 20-C0760

Folsom Dam Civil Maintenance Building – Folsom Unit, American River Division, Central Valley Project, California

Building Solutions, Inc., Reno, NV

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	99.3%
Contractor Earnings:	August	\$0
	Previous	\$6,726,090.55
	Total to Date	\$6,726,090.55

Area Office Project Management

Project Manager: Ed Roza, CC-608

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

No invoices were received this period.

Office Engineering is dealing with completion of final submittals.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Michael E. Manlick, MPCO-313

Number of contract employees: 8

Work Performed:

Subcontractor Rex Moore's fire alarm electrician performed ongoing testing to determine the cause of the continuous triggering of the tamper switch modulator. Rex Moore also verified wiring and worked with Apparatus Testing and Engineering to conduct transformer testing.



Folsom Dam Civil Maintenance Building

An Eaton Corporation electrical technician confirming the power meter in the main distribution panel MDP is installed correctly and functioning properly

Contract No. R12PC20104

Specification No. 20-C0792

Northfork Pipeline Repair Folsom Pumping Plant – Folsom Unit, American River Division,

Central Valley Project, California

Anderson-Burton Construction, Inc., Arroyo Grande, CA

Work Performed:	August	0%
	Time Elapsed	81.8%
	Work Completed	91.9%

Contractor Earnings:	August	\$0
	Previous	\$1,444,543.51
	Total to Date	\$1,444,543.51

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Madelyn Giles, MPCO-210

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Todd Dooley, MPCO-314; Mike Manlick, MPCO-313

Number of Contract Employees: 0

Work Performed:

No work was performed this period. The Contractor demobilized from the jobsite in June 2013 and plans to return November 2013.

Contract No. R13PC20211

Specification No. 20-C0798

New Melones Artifact Storage Building – New Melones Unit, East Side Division, Central Valley Project, California

B. C. Schmidt Construction, Inc., Williams, CA

Work Performed:	August	0%
	Time Elapsed	49.1%
	Work Completed	1.5%
Contractor Earnings:	August	0
	Previous	\$22,503.00
	Total to Date	\$22,503.00

Area Office Project Management

Project Manager: Laureen Perry, MP-153

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Dennis Schuenemann, MPCO-338

Number of Contract Employees: 0

Work Performed:

No site work was performed. The Contractor plans to begin site work in September 2013.

Contract No. R13PC20084

Specification No. 20-C0805

Nimbus Powerplant Transformer Anchorage System – Folsom Unit, American River Division,
Central Valley Project, California

Collins Electrical Company, Inc., Stockton, CA

Work Performed:	August	0%
	Time Elapsed	64.7%
	Work Completed	15.1%

Contractor Earnings:	August	\$0
	Previous	\$23,948.82
	Total to Date	\$23,948.82

Area Office Project Management

Project Manager: Brian Zewe, CC-607A

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Ben Richburg, 338-5117

Number of Contract Employees: 0

Work Performed:

No work was performed this period. Site work is scheduled to begin in October 2013.

Contract No. R13PC20092

Specification No. 20-C0807

Mormon Dam Auxiliary Dam Overlay – Safety of Dams Modification – Folsom Unit, American River Division, Central Valley Project, California

Suulutaaq, Inc. Suisun City, CA

Work Performed:	August	0%
	Time Elapsed	0.6%
	Work Completed	0.8%
Contractor Earnings:	August	\$111,590.00
	Previous	\$0
	Total to Date	\$111,590.00

Area Office Project Management

Project Manager: Chelsea Stewart, CC-417

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

Invoice 1 was received and forwarded to the Denver finance office for processing.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Sean Frische, MPCO-317

Number of Contract Employees: 0

Work Performed:

Site work is scheduled to begin in October 2013.

Contract No. R10PC20859

Specification No. None

Folsom Dam and Powerplant Site Security System – Folsom Unit, American River Division,

Central Valley Project, California

Trofolz Technologies, Inc., Rocklin, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	97.9%

Contractor Earnings:	August	\$0
	Previous	\$6,235,856.32
	Total to Date	\$6,235,856.32

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Administrator: Kevin Jacobs, MPCO-214

No invoices were received this period.

A modification will be processed to extend the period of performance.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Phil Moseby, MPCO-327

Number of Contract Employees: 0

Work Performed:

All site work was completed in December 2012 and the substantially complete date was December 28, 2012.

KBAO

There were no active construction projects underway for the Klamath Basin Area Office in August 2013.

LBAO

Contract No. R12PC20137

Specification No. 20-C0796

Prosser Creek Dam OHV Bridge Crossing – Stampede Division, Washoe Project, California

Algerine West Construction, Inc., Jamestown, CA

Work Performed	August	0%
	Time Elapsed	100%
	Work Completed	0%
Contractor Earnings	August	\$0
	Previous	\$0
	Total to Date	\$0

Area Office Project Management

Project Manager: Locke Hahne, LO-400

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

Invoice 1 was received but rejected because the charges became inaccurate due to the damage the Contractor did to the bridge and end walls, as explained below. A new invoice will be worked out with the Contractor.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Dennis Schuenemann, MPCO-338

Number of Contract Employees: 8

Work Performed:

- Algerine West placed concrete atop each footing at both abutments, placed the concrete apron on the down slope side of the south abutment footing, and placed the concrete approach slabs at both abutments. The Contractor also assembled and installed the Bridge, backfilled and compacted soil around the concrete footings, end walls, and approach slabs, placed and compacted gravel surfacing at the north abutment, completed grading at the north abutment, placed all boulders at the north abutment, and removed spoils piles from the job site and transported them to the waste pile location

On August 21, while the Contractor was moving one end of the bridge, a cable broke injuring a worker and damaging the east end wall at the north abutment. During the following weekend, the Contractor damaged two truss members and the east end wall at the south abutment. MPCO is investigating the incidents and MP-210 will recommend the method of repair.



Prosser Creek Dam OHV Bridge Crossing
Bridge with Timbers secured

NCAO

Contract No. R10PC20744

Specification No. 20-C0712

J.F. Carr Power Plant, Generator G1 and G2 Rewinds – Trinity River Division, Central Valley
Project California

National Electric Coil, Inc., Columbus, OH

Work Performed	August	0%
	Time Elapsed	100%
	Work Completed	96.5%

Contractor Earnings	August	\$0
	Previous	\$14,889,222.14
	Total to Date	\$14,889,222.14

Area Office Project Management

Program Manager: John Dotter, NC-261

Office Engineering

Contract Administrator: Kevin Jacobs, MPCO-214

No invoices were received this period.

We are working with the Contractor on completing outstanding modifications.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Worked Performed:

The Contractor completed all site work in December 2012.

Contract No. R10PC20102

Specification No. 20-C0755

Spring Creek Powerplant Generators G1 and G2 Rewinds – Trinity River Division, Central Valley Project, California

Andritz Hydro Corp., Charlotte, NC

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	69.9%

Contractor Earnings:	August	\$0
	Previous	\$7,923,921.77
	Total to Date	\$7,923,921.77

Area Office Project Management

Project Manager: Joe Ascoli, NC-650

Office Engineering

Contract Administrator: Kevin Jacobs, MPCO-214

No invoices were received this period.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:

No site work was performed this period. Site work will begin again in November 2013.

Contract No. R12PC20044
Specification No. 20-C0774a
Station Service Switchgear Replacement – Trinity River Division, Central Valley Project,
California
Eaton Corporation, Raleigh, NC

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	99.1%

Contractor Earnings:	August	\$0
	Previous	\$2,195,413.41
	Total to Date	\$2,195,413.41

Area Office Project Management
Project Manager: Jeff Gifford, NC-221

Office Engineering
Contract Administrator: Ryan Hennigan, MPCO-211

Notice to Proceed date: April 2, 2012

No invoices were received this period.

The Contractor has only to complete final submittals.

Field Engineering
Construction Manager: Steve Holmes, MPCO-320
Construction Representative: David Derk, MPCO-334

Number of Contract Employees: 0

Worked Performed:
All site work has been completed. The dates of substantial completion were:

<u>Site</u>	<u>Date</u>
Spring Creek	May 5, 2012
JF Carr	February 23, 2013
Trinity	February 15, 2013

Contract No. R12PC20053

Specification No. 20-C0789

Shasta Powerplant Control and Computer Room HVAC Replacement – Shasta Division, Central Valley Project, California

Ray-Mac Mechanical, Inc., Mt. Shasta, CA.

Work Performed:	August	0%
	Time Elapsed	100.0%
	Work Completed	94.3%
Contractor Earnings:	August	\$0
	Previous	\$309,680.00
	Total to Date	\$309,680.00

Area Office Project Management

Project Manager: Bob Gee, NC-230

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

Notice to Proceed date: April 26, 2012

No invoices were received this period.

The Contractor has only to complete final submittals.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:

No site work was performed as the Contractor completed all site work in October 2012. The substantially complete date was October 5, 2012.

Contract No. R10PC20025

Specification No. None

Coleman Fish Hatchery Water Intakes Vegetation Replacement and Monitoring – Shasta

Division, Central Valley Project, California

Tehama Environmental Solutions, Inc., Red Bluff, CA

Work Performed:	August	0%
	Time Elapsed	53.8%
	Work Completed	91.6%
Contractor Earnings:	August	\$0
	Previous	\$648,578.56
	Total to Date	\$648,578.56

Area Office Project Management

Project Manager: Hank Harrington, NC-210

Office Engineering

Contract Administrator: Jacquelyn Olds, MPCO-202

No invoices were received this period.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Fernando Pavone, MPCO-333

Number of Contract Employees: 0

Work performed:

The Contractor's current activity consists of maintaining vegetation it planted in 2010.

Contract No. R11PC20235

Specification No. None

Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation –
Sacramento Canal Units, Sacramento River Division, Central Valley Project, California
Tehama Environmental Solutions, Inc., Red Bluff, CA

Work Performed:	August	0 %
	Time Elapsed	25.1%
	Work Completed	89.1%

Contractor Earnings:	August	\$175,149.49
	Previous	\$4,110,404.04
	Total to Date	\$4,285,553.53

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Administrator: Jacquelyn Olds, MPCO-202

Invoice 11 was received and forwarded to the Denver finance office for processing. It was not for work done this period, but for work done through July 31, 2013.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Fernando Pavone, MPCO-333

Number of Contract Employees: 2

Work performed:

Tehama Environmental Solution irrigated vegetation it had planted and weeded.

SCCAO

Contract No. R11PC20185

Specification No. 20-C0778

Tracy 13.8kV Switchgear/Breaker Replacement – Tracy Pumping Plant and Substation – Delta

Division, Central Valley Project, California

Contra Costa Electric Corp., Martinez, CA

Work Performed:	August	0%
	Time Elapsed	51.6%
	Work Completed	10.4%

Contractor Earnings:	August	\$0
	Previous	\$1,207,280.72
	Total to Date	\$1,207,280.72

Area Office Project Management

Project Manager: Warren Feng, TO-438

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

This is a design/build contract.

No invoices were received this period

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: To Be Determined

Number of Contract Employees: 0

Work performed:

No site work was performed because the Contractor has not yet mobilized to the site. The Contractor is scheduled to begin site work in October 2013.

Contract No. R12PC20062

Specification No. 20-C0785

Tracy Fish Collection Facility - Trash Rake Monorail Extension – Delta Division, Central Valley Project, California

Monterey Mechanical Co., Oakland, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	90.1%

Contractor Earnings:	August	\$0
	Previous	\$658,756.43
	Total to Date	\$658,756.43

Area Office Project Management

Project Manager: David Tsao, TO-435

Office Engineering

Contract Administrator: Larry Bowman, MPCO-240

No invoices were received this period.

The Contractor has only to complete final submittals.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:

No site work was performed this period as site work is complete and the date of substantial completion was April 24, 2013.

Contract No. R12PC20107

Specification No. 20-C0788

San Luis Demonstration Treatment Plant – San Luis Unit Drainage –
– San Luis Unit, West Stanislaus Division, Central Valley Project, California
Slayden Construction Group, Inc., Stayton, OR

Work Performed:	August	0%
	Time Elapsed	56.1%
	Work Completed	18.4%
Contractor Earnings:	August	\$1,362,309.92
	Previous	\$4,119,899.83
	Total to Date	\$5,482,209.75

Area Office Project Management

Project Manager: Cheryl Carter, SCC-105

Office Engineering

Contract Administrator: Casandra Arthur, MPCO-245

Invoice 8 was received and forwarded to the Denver finance office for processing. It was not for work done this period, but for work through July 31, 2013.

Field Engineering

Construction Manager: Dave Arter, MPCO-315

Onsite Government Representative: John Nelson, MPCO-328

Project Engineer: Chris Van Deusen, MPCO-345

Construction Control Inspector: Philip H. Vanderwal

Number of Contract Employees: 30

Work performed:

Slayden Construction Group prepared foundations for various structures, set forms and placed concrete, and continued to install yard pipe as required throughout the treatment area, then placed and compacted backfill

CMC Rebar

Ironworkers placed and tied rebar for treatment building slabs and trench walls.

Triple C

The crew of finishers applied the required finish to the completed placements.

Con J Franke Electrical

Electricians continued installation of ground wire and risers as placements progressed. They also continued to install conduit for various electrical runs.

O'Dell Engineering

O'Dell Engineering provided Stormwater Pollution Prevention Plan inspections and monitoring as required. They also provided quantity surveys and control points for construction activities and construction surveys for the line and grade of the tile sump lateral piping.

McElvany, Inc.

The crew fused high density polyethylene (HDPE) pipe and performed the simultaneous process of trenching, laying, and bedding the pipe for the long straight sections of the laterals. They then placed backfill over the pipe. Intersections of laterals and ditch crossings are scheduled for a later date when ground water levels are lower.

North State Erectors

The crew of ironworkers began erection of the treatment building columns and framing members.

Mason Painting

The painters utilized pressure washers to clean exposed steel building framing members in preparation for Tabulation No. 1 coating.

Cosco Fire Protection

Workers installed fire protection systems in various areas.



San Louis Demonstration Treatment Plant
Treatment Building

Contract No. R13PC20194

Specification No. 20-C0800

Tracy Facility Pavement Rehabilitation – Delta Division, Central Valley Project, California

Allright Construction, Inc., Kerman, CA

Work Performed	August	0%
	Time Elapsed	31.0%
	Work Completed	14.8%

Contractor Earnings	August	\$219,045.30
	Previous	\$90,237.70
	Total to Date	\$309,283.00

Area Office Project Management

Project Manager: Brian Shinmoto, TO-430

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

Invoice 3 was received and forwarded to the Denver finance office for processing. It was not for work done this period, but for work through July 31, 2013.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 7

Worked Performed:

The asphalt concrete placement at the Antioch site was completed.

At the Tracy site, Allright Construction removed the smaller asphalt sections around the buildings and placed the first 2-inch lift of asphalt in these sections.

On Lindemann Road, the existing base material was removed and replaced with new base material. It was then compacted, with compaction verified by a third party inspection service.

The drainage ditch excavation was started at the lowest point and workers were working towards the north to a higher elevation.



Tracy Facility Pavement Rehabilitation
Allright Construction laborers excavating asphalt concrete pavement at Tracy site

Regional

Contract No. R10PC20R42

Specification No. 20-C0746

Hydropower Facility Modifications - Stage 1 – ARRA Project No. 14.000 - Battle Creek Salmon and Steelhead Restoration Project, California

RTA Construction/Ray Toney JV, Redding, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	100%

Contractor Earnings:	August	\$0
	Previous	\$10,189,508.44
	Total to Date	\$10,189,508.44

Regional Office Project Management

Project Manager: Mary Marshall, MP-203

Office Engineering

Contract Administrator: Kent Perkes, MPCO-225

No invoices were received this period.

The Contractor has to complete final submittals. A claim remains to be resolved.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: John Pospishil, MPCO-321

Field Inspectors: Jason Foust, MPCO-325

Number of Contract Employees: 0

Work performed:

The Contractor completed all site work in March 2013 and the substantially complete date was March 15, 2013.

Contract No. R10PC20R80

Specification No. 20-C0759

Drought Relief – Construction of New Wells – ARRA Project No. 28.002 – California

Layne Christensen Company, Fontana, CA

Work Performed:	August	0%
	Time Elapsed	100%
	Work Completed	96.2%

Contractor Earnings:	August	\$0
	Previous	\$15,402,308.57
	Total to Date	\$15,402,308.57

Regional Office Project Management

Project Manager: Kevin Clancy, MP-410

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

No invoices were received this period.

The Contractor has only to complete final submittals.

Field Engineering

Construction Manager: John E. Nelson, MPCO-328

Construction Representative: John E. Nelson, MPCO-328

Number of Contract Employees: 0

Work performed:

No site work was performed this period. The remaining work consists of punch list items.

Contract No. R13PC20005

Specification No. 20-C0799

Baldwin Creek Fish Barrier – Battle Creek Salmon and Steelhead Restoration Project, California

Contractor Services Group, Inc.

Work Performed:	August	0%
	Time Elapsed	54.8%
	Work Completed	38.4%

Contractor Earnings:	August	\$863,565.56
	Previous	\$519,911.35
	Total to Date	\$1,383,476.91

Regional Office Project Management

Project Manager: Mary Marshall, MP-203

Office Engineering

Contract Administrator: Kent Perkes, MPCO-225

Invoice 4 was received and forwarded to the Denver finance office for processing. It was not for work done this period, but for work through July 31, 2013.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: John Pospishil, MPCO-321

Construction Inspector: Jason Foust, MPCO-325; Jeff Kelly, MPCO-361

Number of Contract Employees: 20

Work performed:

The Contractor completed the diversion system this period and has been monitoring the pumps and generators during the night hours. They also finished excavating the smooth apron and the 2:1 slope between the concrete slope-protection, hauled the spoils from the excavation to Use Area 11E, where they were stockpiled, and placed, finished, cured, and patched concrete for the Barrier Weir Placements 1-1, 1-7, 1-3, and 1-9.



Baldwin Creek Fish Barrier
Laborer removing rock with a jackhammer

Contracts in Warranty Status

R09PC20R03 20-C0677 Transformer K1A and K2A Replacements, Folsom Power Plant

There was no Office Engineering Administrative activity this period.

5-year warranty for K1A extends to January 30, 2016, and that for K2A extends to January 4, 2017.

R10PC20R11 20-C0730 Red Bluff Pumping Plant and Fish Screen, Pumps and Motors

There was no Office Engineering Administrative activity this period.

3-year warranty extends to August 2015.

R10PC20R32 20-C0749 Fish Screen Structure Phase 3, Contra Costa Canal

1-year warranty for M340 CPU located inside the SCADA panel extends to March 20, 2013.

1-year warranty for Siemens ultrasonic level transmitter extended to August 21, 2013.

R10PX20R54 20-C0750 Drought Relief, Well Enhancements

There was no Office Engineering Administrative activity this period.

1-year warranty extends to December 6, 2013.

R10PC20R33 20-C0752 Red Bluff Pumping Plant and Fish Screen

Closeout submittals were dealt with this period.

1-year warranty extends to September 26, 2013.

R10PC80R23 20-C0761 Delta-Mendota Canal–California Aqueduct Intertie

The final submittal was received and approved this period.

R10PC20197 20-C0768 Control, Upgrade and Modernization of the Gantry and Bridge Cranes at the Folsom Dam and Powerplant

There was no Office Engineering Administrative activity this period.

2-year warranty extends to September 7, 2013.

R11PC20158 20-C0777 Stampede Powerplant and Switchyard Recoatings

There was no Office Engineering Administrative activity this period.

1-year warranty extended to August 12, 2013.

R11PC20124 20-C0780 Coleman National Fish Hatchery Barrier Weir Site Modifications

There was no Office Engineering Administrative activity this period.

1-year warranty extends to September 28, 2013.

R12PC20193 20-C0791 Shasta Dam Traffic Circle Pavement Rehabilitation

There was no Office Engineering Administrative activity this period.

1-year warranty extended to August 4, 2013.
