

RECLAMATION

Managing Water in the West

MP CONSTRUCTION OFFICE

Willows, California

Construction Progress Report – L29

May 2013



San Luis Demonstration Treatment Plant – San Luis Unit Drainage
Placing the Slab at the Main Treatment Building

"Doing It Right from the Start"



U.S. Department of the Interior
Bureau of Reclamation
Mid-Pacific Region

CONSTRUCTION PROGRESS REPORT (L-29)
MP CONSTRUCTION OFFICE
MID-PACIFIC REGION
May 2013

CONTENTS

	PAGE
LOCATION MAP.....	i
STAFFING.....	ii
GLOSSARY OF TERMS.....	iii

<u>CONTRACT/SPECS OR P.O. NO., CONTRACTOR, AND CONTRACT NAME</u>	<u>PAGE</u>	<u>MAP</u>
	<u>NO.</u>	<u>NO.</u>
CCAO	1	
R10PC20R15 20-C0649A Abide International, Inc. Fixed Wheel Gate Rehabilitation – Folsom Unit, American River Division, Central Valley Project, California	3	1
R10PC20019 20-C0689 Andritz Hydro Corp. Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement – Folsom Unit, American River Division, Central Valley Project, California	4	1
R10PC20767 20-C0703 Voith Siemens Hydro Power Generation, Inc. Folsom Power Plant U1, U2, and U3 Replacement Runners – Folsom Unit, American River Division, Central Valley Project, California	6	1
R09PC20171 20-C0720 Perryman Mechanical, Inc. Nimbus Powerplant HVAC System Modification – Folsom Unit, American River Division, Central Valley Project, California	7	2
R10PC20114 20-C0754 Shimmick Construction Co., Inc. Folsom Dam – Safety of Dams Modification – MIAD Key-Block – Folsom Unit, American River Division, Central Valley Project, California	8	1
R10PC20R57 20-C0760 Building Solutions, Inc. Folsom Dam Civil Maintenance Building – Folsom Unit, American River Division, Central Valley Project, California	9	1
R12PC20104 20-C0792 Anderson-Burton Construction Northfork Pipeline Repair - Folsom Pumping Plant – Folsom Unit, American River Division, Central Valley Project, California	10	1
R13PC20211 20-C0798 B.C Schmidt Construction, Inc. New Melones Artifact Storage Building – New Melones Unit, East Side Division, Central Valley Project, California	12	3
R10PC20859 None Trofholz Technologies, Inc. Folsom Dam and Powerplant Site Security System – Folsom Unit, American River Division, Central Valley Project, California	13	1

KBAO			15
LBAO			19
R12PC20137	20-C0796	Algerine West Construction, Inc. Prosser Creek Dam OHV Bridge Crossing – Stampede Division, Washoe Project, California	21 4
NCAO			21
R10PC20744	20-C0712	National Electric Coil, Inc. J.F. Carr Power Plant, Generator G1 and G2 Rewinds – Trinity River Division, Central Valley Project California	25 5
R10PC20102	20-C0755	Andritz Hydro Corp. Spring Creek Powerplant Generators G1 and G2 Rewinds – Trinity River Division, Central Valley Project, California	26 5
R12PC20044	20-C0774a	Eaton Corp. Station Service Switchgear Replacement – Trinity River Division, Central Valley Project, California	27 5, 6
R12PC20053	20-C0789	Ray-Mac Mechanical, Inc. Shasta Powerplant Control and Computer Room HVAC Replacement – Shasta Division, Central Valley Project, California	28 6
R10PC20025	None	Tehama Environmental Solutions, Inc. Coleman Fish Hatchery Water Intakes Vegetation Replacement and Monitoring – Shasta Division, Central Valley Project, California	29 7
R11PC20235	None	Tehama Environmental Solutions, Inc. Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation – Sacramento Canals Unit, Sacramento River Division, Central Valley Project, California	30 8
SCCAO			33
R10PC80R23	20-C0761	Shimmick Construction Co., Inc. Delta-Mendota Canal–California Aqueduct Intertie – Central Valley Project – California	35 9
R11PC20185	20-C0778	Contra Costa Electric Corp. Tracy 13.8kV Switchgear/Breaker Replacement – Tracy Pumping Plant and Substation – Delta Division, Central Valley Project, California	36 10
R12PC20062	20-C0785	Monterey Mechanical Co. Tracy Fish Collection Facility – Trash Rake Monorail Extension – Delta Division Central Valley Project, California	37 10
R11PC20107	20-C0788	Slayden Construction Group, Inc. San Luis Demonstration Treatment Plant – San Luis Unit Drainage – San Luis Unit, West Stanislaus Division, Central Valley Project, California	38 11
R13PC20194	20-C0800	Allright Construction, Inc. Tracy Facility Pavement Rehabilitation – Delta Division, Central Valley Project, California	39 10, 12

Regional	41
R10PC20R42 20-C0746 RTA Construction/Ray Toney JV Hydropower Facility Modifications-Stage 1 – Battle Creek Salmon and Steelhead Restoration Project, California	43
R10PC20R80 20-C0759 Layne Christensen Co. Drought Relief–Construction of New Wells–ARRA Project No. 28.002–California	44
R13PC20005 20-C0799 Contractor’s Services Group, Inc. Baldwin Creek Fish Barrier – Battle Creek Salmon and Steelhead Restoration Project, California	45
R13PX20026 20-C0806 CW Crosser Construction, Inc. Pixley National Wildlife Refuge Alfalfa Valve Modifications – California	46
 Contracts in Warranty Status	 49
R09PC20R03 20-C0677 Transformer K1A and K2A Replacements, Folsom Power Plant	51
R10PC20128 20-C0706 New Melones Power Plant Excitation System Replacement	51
R10PC20R11 20-C0730 Red Bluff Pumping Plant and Fish Screen, Pumps and Motors	51
R10PX20R45 20-C0750 Drought Relief, Well Enhancements	51
R10PX20R54 20-C0750 Drought Relief, Well Enhancements	51
R10PC20R33 20-C0752 Red Bluff Pumping Plant and Fish Screens	51
R10PC20197 20-C0768 Control, Upgrade and Modernization of the Gantry and Bridge Cranes at the Folsom Dam and Powerplant	51
R10PC20196 20-C0769 Control Upgrade and Modernization of the Gantry Crane at Nimbus Powerplant	51
R12PC20055 20-C0776b Delta Cross Channel Gate Hoist Wire Rope Replacement	51
R12PC20158 20-C0777 Stampede Powerplant and Switchyard Recoatings	51
R11PC20124 20-C0780 Coleman National Fish Hatchery Barrier Weir Site Modifications	52

R12PC20193 20-C0791
Shasta Dam Traffic Circle Pavement Rehabilitation


52

R10PC20R32 20-C0749
Fish Screen Structure Phase 3, Contra Costa Canal

52

Mid-Pacific Region

RECLAMATION
Managing Water in the West

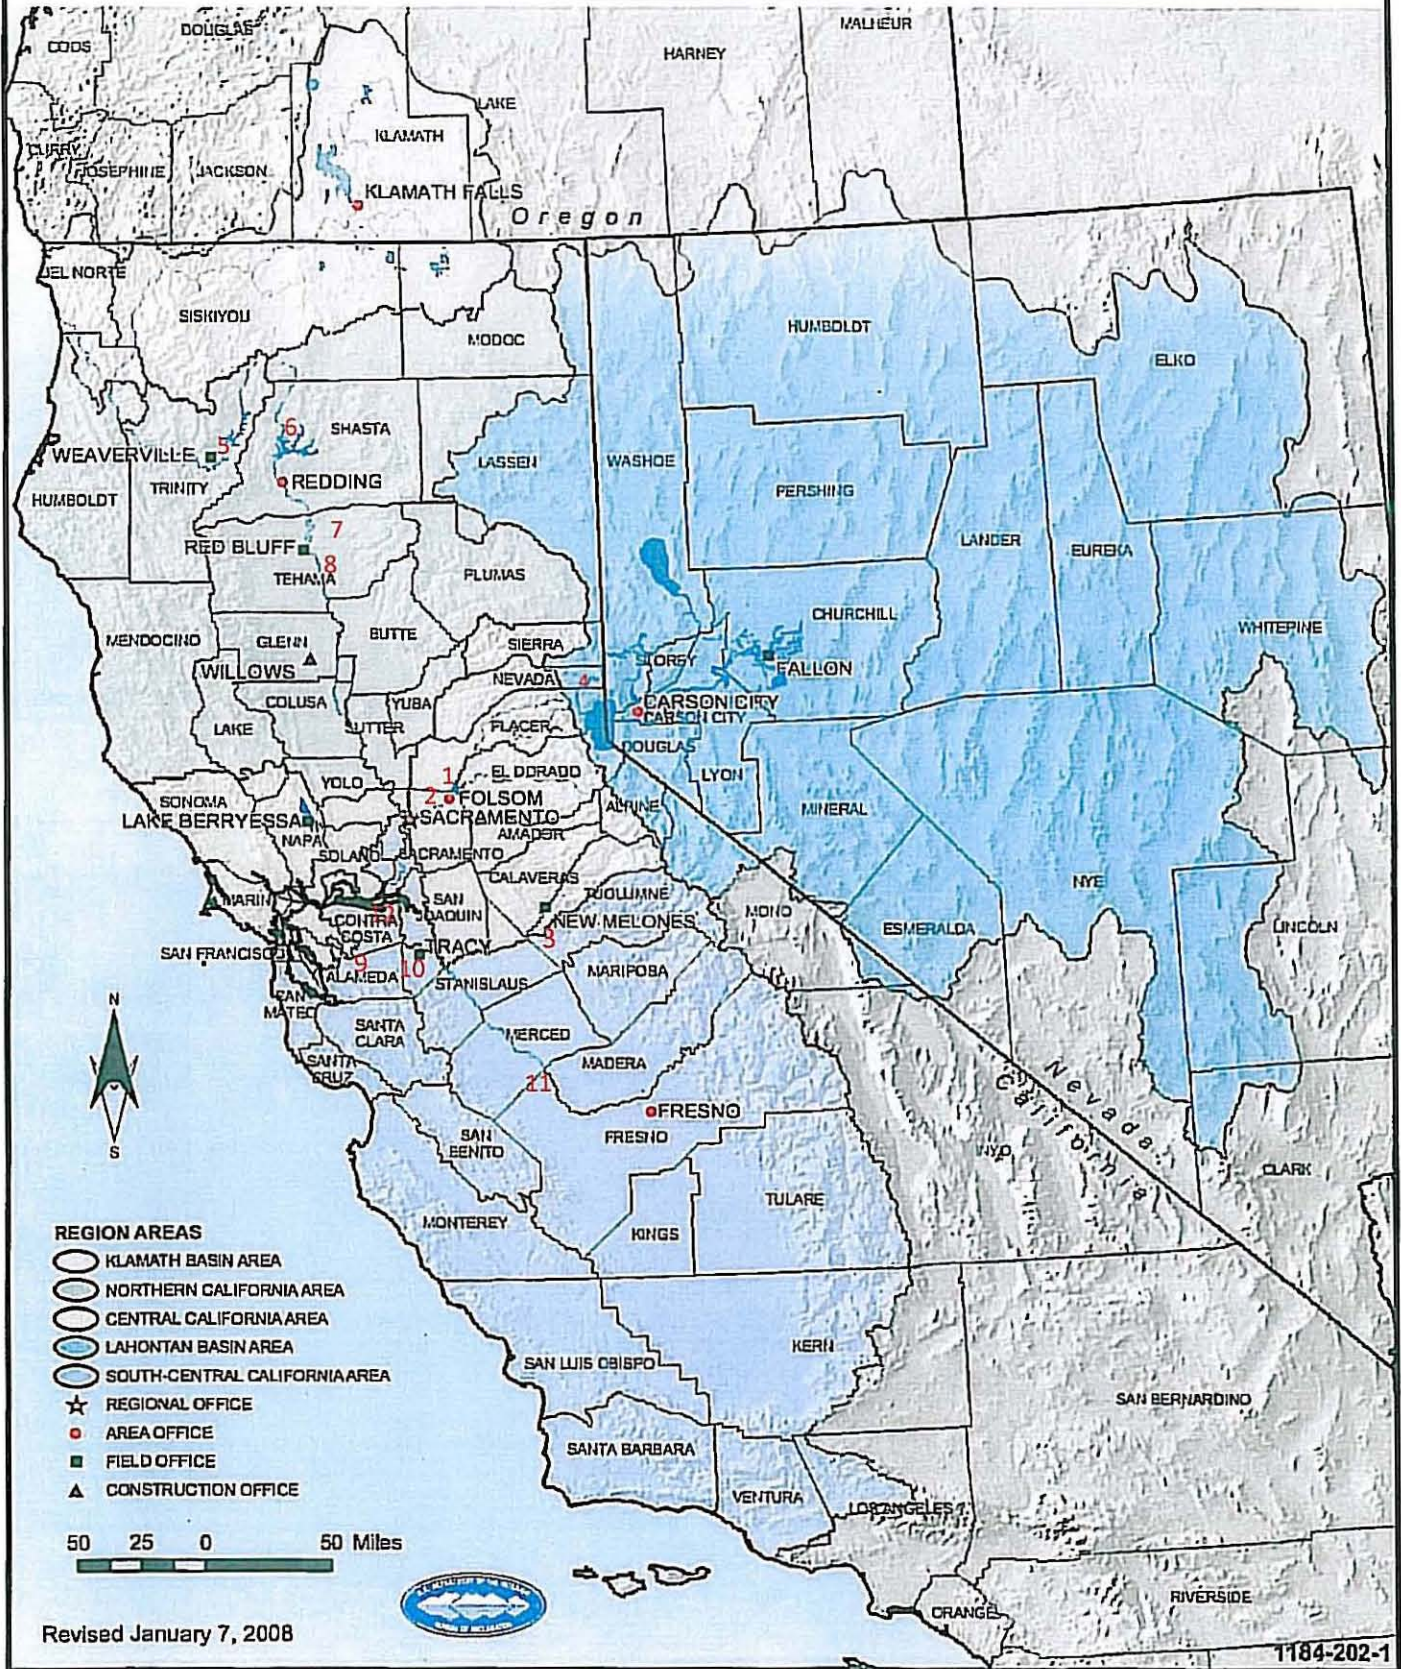

STAFFING – MID PACIFIC CONSTRUCTION OFFICE

The Mid Pacific Construction Office had 61 construction and administrative employees at the close of this month as follows:

Construction Engineer's Office	2
Preaward & Project Management Group	3
Administrative Management	10
Division of Field Engineering	28
Division of Office Engineering	11
Materials Lab Branch	7

GLOSSARY OF ACRONYMS AND ABBREVIATIONS

MEANING

ARRA	American Recovery and Reinvestment Act
CCAO	Central California Area Office
CVP	Central Valley Project
KBAO	Klamath Basin Area Office
LBAO	Lahontan Basin Area Office
MP	Mid Pacific Regional Office
MPCO	Mid-Pacific Construction Office
NCAO	Northern California Area Office
SCCAO	South Central California Area Office
TO	Tracy Office

CCAO

Contract No. R10PC20R15

Specification No. 20-C0649A

Fixed Wheel Gate Rehabilitation – American River Division – Folsom Unit - Central Valley

Project, California

Abide International, Inc., Sonoma, CA

Work Performed:	May	0%
	Time Elapsed	91.8%
	Work Completed	78.4%
Contractor Earnings:	May	\$158,172.17
	Previous	\$6,487,353.29
	Total to Date	\$6,645,525.46

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Larry Bowman, MPCO-240

Invoice 8 was received and forwarded to the Denver finance office for processing. It was not for work done this period but was for work done through April 30, 2013.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Gustavo Aguilera, MPCO-337

Number of Contract Employees: 10

Work performed:

Most of the work performed was under Modification 6. Under Modification 6 the seals for Gates 1 and 2 were successfully seated on the dam wall, and the hydraulic cylinders on Gates 1 and 2 were surveyed to determine the overall cylinder lengths.

Under Modification 5, and as a temporary fix, the hydraulic system was adjusted to increase the operation speed to protect the equipment.

Under the base contract Jeffco Painting and Coating coated Gates 1 and 2.

Contract No. R10PC20019

Specification No. 20-C0689

Folsom Power Plant Generators U1, U2, and U3 Rewind and Excitation System Replacement –

American River Division – Folsom Unit – Central Valley Project, California

Andritz Hydro Corp, Charlotte, NCFolsom Fixed Wheel Gate Rehabilitation

Work Performed:	May	0%
	Time Elapsed	70.5%
	Work Completed	68.6%

Contractor Earnings:	May	\$0
	Previous	\$13,631,783.42
	Total to Date	\$13,631,783.42

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Madelyn Giles, MPCO-210

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Sergio Vivar, MPCO-311, Todd Dooley, MPCO-314

Number of Contract Employees: 5

Work performed:

Andritz Hydro performed the following work:

- Continued installation of Unit 1 non-segregated AC and DC buses
- Positioned and secured the power potential transformer (PPT) and exciter in their final locations on the equipment platform
- Finished installation of the last two conduit runs from the exciter to the PPT
- Modified and re-installed the existing non-segregated AC bus protection screen inside the air housing
- Repainted scuffed areas on the rotor poles



Folsom Power Plant Generators U1, U2, and U3 Rewind and
Excitation System Replacement
The installed AC and DC bus system

Contract No. R10PC20767

Specification No. 20-C0703

Folsom Power Plant U1, U2, and U3 Replacement Runners – American River Division – Folsom Unit – Central Valle-y Project, California

Voith Siemens Hydro Power Generation, Inc., York, PA

Work Performed:	May	0%
	Time Elapsed	87.6%
	Work Completed	73.3%

Contractor Earnings:	May	\$0
	Previous	\$5,419,539.62
	Total to Date	\$5,419,539.62

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Madelyn Giles, MPCO-210

No invoices were received this period.

Field Engineering

Construction Manager: N/A supply contract

Construction Representative: N/A supply contract

Number of Contract Employees: N/A supply contract

Work performed: N/A supply contract

Contract No. R09PC20171

Specification No. 20-C0720

Nimbus Powerplant HVAC System Modification – American River Division – Folsom Unit,

Central Valley Project, California

Perryman Mechanical, Inc., West Sacramento, CA

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	79.9%
Contractor Earnings:	May	\$0
	Previous	\$428,963.09
	Total to Date	\$428,963.09

Area Office Project Management

Brian Zewe, CC-607A

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

No invoices were received this period.

The contractor has only to complete overdue submittals and conduct training and is expected to complete submittal requirements in the next few months.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Todd Dooley, MPCO-314

Number of Contract Employees: 0

Work performed:

All site work has been completed and the substantially complete date is December 17, 2010.

Contract No. R10PC20114

Specification No. 20-C0754

Folsom Dam – Safety of Dams Modification – MIAD Key-Block – American River Division,

Folsom Unit, Central Valley Project, California.

Shimmick Construction Co., Inc., Sacramento, CA

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	94.9%
Contractor Earnings:	May	\$10,00.00
	Previous	\$43,172,626.23
	Total to Date	\$43,182,626.23

Area Office Project Management

Project Manager: Larry Hobbs, CC-106

Office Engineering

Contract Administrator: Larry Bowman, MPCO-240

Invoice 32 was received and forwarded to the Denver finance office for processing. It was not for work done this period but was for work done through March 28, 2013.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Howard Diedrich, MPCO-316, Sean Frische, MPCO-317

Number of Contract Employees: 0

Work Performed:

No site work was performed as all site work was complete in February 2013. The substantial completion date is January 4, 2013.

Contract No. R10PC20R57

Specification No. 20-C0760

Folsom Dam Civil Maintenance Building – American River Division – Folsom Unit - Central Valley Project, California

Building Solutions Inc., Reno, NV

Work Performed:	December	0%
	Time Elapsed	100%
	Work Completed	99.3%

Contractor Earnings:	December	\$0
	Previous	\$6,726,090.55
	Total to Date	\$6,726,090.55

Area Office Project Management

Project Manager: Ed Roza, CC-608

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

No invoices were received this period.

The contractor has only to complete final submittals.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Michael E. Manlick, MPCO-313

Number of contract employees: 0

Work Performed:

No work was performed this period and the contractor has only to complete punch list items.

Contract No. R12PC20104

Specification No. 20-C0792

Northfork Pipeline Repair Folsom Pumping Plant – American River Division, Folsom Unit,
Central Valley Project, California.

Anderson-Burton Construction, Inc., Arroyo Grande, CA

Work Performed:	May	39.3%
	Time Elapsed	98.1%
	Work Completed	75.1%
Contractor Earnings:	May	\$505,948.78
	Previous	\$460,149.91
	Total to Date	\$966,098.69

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Madelyn Giles, MPCO-210

Invoice 2 was received and forwarded to the Denver finance office for processing.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Todd Dooley, MPCO-314

Number of Contract Employees: 27

Work Performed:

JM Environmental performed the following:

- Detailing of the interior areas where coal tar was removed and on the expansion joint and weld repair blisters in preparation for epoxy touch-up
- Lead remediation at expansion joints at the east side of the project
- Removal of damaged top and intermediate coatings while minimizing the disturbance of the lead based prime coating

American, Inc. performed the following:

- Remediation work on all the manway butt strap end welds
- Successfully air testing of butt strap welds for the three manways
- Installation of the following:
 - Packing rings in the expansion joints
 - Air relief valve V61 on the 84" pipeline, west of the downstream coupling
 - Victaulic couplings on both pipe unions
 - Gaskets and blind flanges on the manways

ABCI performed the following:

- Completion of weld repairs to the wastage areas of the pipeline
- Swept-blasted the pipeline for epoxy coating
- Performed remediation work on the improperly batched epoxy coating
- Brought an additional coatings consultant on site to facilitate better inspection and testing of the coating
- Final inspection for holidays and mil thickness
- Replacement of the 48' blind flange on the pipeline stub at the Hinkle Wye

Pro Finish performed the following:

- Assisted in abrasive blasting of the pipeline
- Prepared the deficient painted areas for recoating
- Epoxy coated the pipe ends at expansion joints, couplings, pipe ends, butt straps on manways, and at repair areas

Miscellaneous:

On Friday, May 31st, pipe re-watering was completed



Northfork Pipeline Repair Folsom Pumping Plant
Coatings consultant performing a surface profile test on the pipeline interior

Contract No. R13PC20211

Specification No. 20-C0798

New Melones Artifact Storage Building – East Side Division, New Melones Unit, Central Valley Project, California.

B. C. Schmidt Construction, Inc., Williams, CA

Work Performed:	April	0%
	Time Elapsed	16.0%
	Work Completed	0%
Contractor Earnings:	April	\$0
	Previous	\$0
	Total to Date	\$0

Area Office Project Management

Project Manager: Jesse Castro, CC-607

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

No invoices were received this period.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Dennis Schuenemann, MPCO-338

Number of Contract Employees: 0

Work Performed:

Stantec surveyors gathered topography data at the site. The contractor scheduled site work to begin in July 2013.

Contract No. R10PC20859

Specification No. None

Folsom Dam and Powerplant Site Security System – American River Division – Folsom Unit -
Central Valley Project, California

Trofholtz Technologies, Inc., Rocklin, CA

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	97.9%
Contractor Earnings:	May	\$0
	Previous	\$6,235,856.94
	Total to Date	\$6,235,856.94

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Administrator: Kevin Jacobs, MPCO-214

No invoices were received this period.

A modification is being prepared to extend the contract completion date.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Phil Moseby, MPCO-327

Number of Contract Employees: 0

Work Performed:

All site work was completed in December 2012 and the substantially complete date is December 28, 2012.

KBAO

There were no active construction projects underway for the Klamath Basin Area Office in October 2012.

LBAO

Contract No. R12PC20137

Specification No. 20-C0796

Prosser Creek Dam OHV Bridge Crossing – Stampede Division – Washoe Project, California

Algerine West Construction, Inc., Jamestown, CA

Work Performed	May	0%
	Time Elapsed	39.3%
	Work Completed	0%
Contractor Earnings	May	\$0
	Previous	\$0
	Total to Date	\$0

Area Office Project Management

Project Manager: Locke Hahne, LO-400

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

Notice to Proceed was issued on April 2, 2013.

Invoice 1 was received this period but was returned as improper.

Field Engineering

Construction Manager: Henry Garcia, MPCO-310

Construction Representative: Dennis Schuenemann, MPCO-338

Number of Contract Employees: 0

Worked Performed:

The contractor has scheduled site work to begin the first week of June 2013.

NCAO

Contract No. R10PC20744

Specification No. 20-C0712

J.F. Carr Power Plant, Generator G1 and G2 Rewinds – Trinity River Division – Central Valley
Project, California

National Electric Coil, Inc., Columbus, OH

Work Performed	May	0%
	Time Elapsed	100%
	Work Completed	98.2%

Contractor Earnings	May	\$0
	Previous	\$14,947,810.48
	Total to Date	\$14,947,810.48

Area Office Project Management

Project Manager: John Dotter, NC-261

Office Engineering

Contract Administrator: Kevin Jacobs, MPCO-214

No invoices were received this period.

All that remains is the completion of three modifications and final submittals.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Worked Performed:

The contractor completed all site work in December 2012.

Contract No. R10PC20102

Specification No. 20-C0755

Spring Creek Powerplant Generators G1 and G2 Rewinds – Trinity River Division – Central Valley Project, California

Andritz Hydro Corp., Charlotte, NC

Work Performed:	May	3.1%
	Time Elapsed	97.2%
	Work Completed	69.9%
Contractor Earnings:	May	\$348,180.00
	Previous	\$7,575,741.77
	Total to Date	\$7,923,921.77

Area Office Project Management

Project Manager: Joe Ascoli, NC-650

Office Engineering

Contract Administrator: Kevin Jacobs, MPCO-214

Invoice 6 was received and forwarded to the Denver finance office for processing.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:

No site work was performed this period. Site work will begin again in November 2013.

Contract No. R12PC20044

Specification No. 20-C0774a

Station Service Switchgear Replacement – Trinity River Division – Central Valley Project,
California

Eaton Corporation, Raleigh, NC

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	99.1%

Contractor Earnings:	May	\$0
	Previous	\$2,195,413.41
	Total to Date	\$2,195,413.41

Area Office Project Management

Project Manager: Jeff Gifford, NC-221

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

Notice to Proceed date: April 2, 2012

No invoices were received this period.

The contractor has only to complete final submittals.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Worked Performed:

All site work has been completed. The dates of substantial completion are:

<u>Site</u>	<u>Date</u>
Spring Creek	5/0512
JF Carr	2/23/13
Trinity	2/15/13

Contract No. R12PC20053

Specification No. 20-C0789

Shasta Powerplant Control and Computer Room HVAC Replacement – Shasta Division –

Central Valley Project, California

Ray-Mac Mechanical, Inc., Mt. Shasta, CA.

Work Performed:	January	0%
	Time Elapsed	100%
	Work Completed	94.3%

Contractor Earnings:	January	\$0
	Previous	\$309,680.00
	Total to Date	\$309,680.00

Area Office Project Management

Project Manager: Bob Gee, NC-230

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

Notice to Proceed date: April 26, 2012

No invoices were received this period.

The contractor has only to complete final submittals.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:

No site work was performed as the contractor completed all site work in October 2013. The substantially complete date is October 5, 2013.

Contract No. R10PC20025

Specification No. None

Coleman Fish Hatchery Water Intakes Vegetation Replacement and Monitoring – Shasta

Division – Central Valley Project, California

Tehama Environmental Solutions, Inc., Red Bluff, CA

Work Performed:	May	3.2%
	Time Elapsed	49.1%
	Work Completed	91.6%
Contractor Earnings:	May	\$22,483.25
	Previous	\$626,095.31
	Total to Date	\$648,578.56

Area Office Project Management

Project Manager: Hank Harrington, NC-210

Office Engineering

Contract Administrator: Jacquelyn Olds, MPCO-202

Invoice 18 was received and forwarded to the Denver finance office for processing.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Daniel Pavone, MPCO-333

Number of Contract Employees: 0

Work performed:

The contractor's current activity consists of maintaining vegetation it planted in 2010.

Contract No. R11PC20235

Specification No. None

Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation –
Sacramento Canal Units – Sacramento River Division – Central Valley Project, California
Tehama Environmental Solutions, Inc., Red Bluff, CA

Work Performed:	May	0%
	Time Elapsed	20.8%
	Work Completed	78.7%
Contractor Earnings:	May	\$0
	Previous	\$3,781,257.36
	Total to Date	\$3,781,257.36

Area Office Project Management

Project Manager: Bill Vanderwaal, MPCO-122

Office Engineering

Contract Administrator: Jacquelyn Olds, MPCO-202

No invoices were received this period.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: Daniel Pavone, MPCO-333

Number of Contract Employees: 4

Work performed:

The contractor maintained the planted areas. During irrigation the well went dry. The contractor will modify watering to prevent this in the future.

The contractor had a botanist onsite teaching its workers how to identify the native and exotic plants to ensure the crew only removes the latter.



Red Bluff Diversion Dam, Fish Passage Improvement Project, Terrestrial Mitigation
The contractor's crew watering the Mix Riparian Forest at the northern island

SCCAO

Contract No. R10PC80R23

Specification No. 20-C0761

Delta-Mendota Canal-California Aqueduct Intertie – Central Valley Project, California

Shimmick Construction Company, Inc., Tracy, CA

Work Performed:	May	1.0%
	Time Elapsed	100%
	Work Completed	99.9%

Contractor Earnings:	May	\$160,142.20
	Previous	\$15,381,816.97
	Total to Date	\$15,541,959.17

Area Office Project Management

Project Manager: Erika Kegel, MP-730

Office Engineering

Contract Administrator: Ryan Hennigan, MPCO-211

Invoice 21 was received and forwarded to the Denver finance office for processing.

The contractor has only to complete one final submittal.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Chris Van Deusen, MPCO-345

Number of Contract Employees: 0

Work performed:

All site work was completed in May 2012. The date of substantial completion is April 6, 2012.

Contract No. R11PC20185

Specification No. 20-C0778

Tracy 13.8kV Switchgear/Breaker Replacement – Tracy Pumping Plant and Substation – Central Valley Project, California

Contra Costa Electric Corp., Martinez, CA

Work Performed:	May	0%
	Time Elapsed	44.9%
	Work Completed	10.4%

Contractor Earnings:	May	\$0
	Previous	\$1,207,280.72
	Total to Date	\$1,207,280.72

Area Office Project Management

Project Manager: Warren Feng, TO-438

Office Engineering

Contract Administrator: Amber Pierce, MPCO-205

This is a design build contract.

No invoices were received this period

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: David Derk, MPCO-334

Number of Contract Employees: 0

Work performed:

No site work was performed because the contractor has not yet mobilized to the site. The contractor is scheduled to begin site work in October 2013.

Contract No. R12PC20062

Specification No. 20-C0785

Tracy Fish Collection Facility - Trash Rake Monorail Extension – Delta Division – Central Valley Project, California

Monterey Mechanical Co., Oakland, CA

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	90.1%
Contractor Earnings:	May	\$656,500.00
	Previous	\$593,256.43
	Total to Date	\$658,756.43

Area Office Project Management

Project Manager: David Tsao, TO-435

Office Engineering

Contract Administrator: Larry Bowman, MPCO-240

Invoice 5 was received and forwarded to the Denver finance office for processing. It was not for work done this period but was for work done through April 30, 2013.

The contractor has only to complete final submittals.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Work performed:

Site work was completed in April 2013, and the substantially complete date is April 24, 2013.

Contract No. R12PC20107

Specification No. 20-C0788

San Louis Demonstration Treatment Plant – San Luis Unit Drainage –
West Stanislaus Division – San Louis Unit – Central Valley Project, California
Slayden Construction Group, Inc., Stayton, OR

Work Performed:	May	0%
	Time Elapsed	43.7%
	Work Completed	12.2%
Contractor Earnings:	May	\$0
	Previous	\$2,730,774.28
	Total to Date	\$2,730,774.28

Area Office Project Management

Project Manager: Cheryl Carter, SCC-105

Office Engineering

Contract Administrator: Casandra Arthur, MPCO-245

No invoices were received this period.

Field Engineering

Construction Manager: John Nelson, MPCO-328

Construction Representative: Chris Van Deusen, MPCO-345

Number of Contract Employees: 15

Work performed:

Slayden Construction Group, Inc. forces continued foundation preparation for building slabs and trenches, setting forms, and completing placements for both treatment building slabs and utility trench walls. Plumbers installed embedded plumbing and fixtures.

CMC Rebar ironworkers placed and tied rebar for treatment building slabs and trench walls.

Triple C Inc. applied the required finish to the completed placements.

Con J Franke Electrical electricians continued installation of ground loop and risers as placements progressed. They also continued installing conduit for various electrical runs embedded in slabs and to runs to outlying treatment areas.

O'Dell Engineering provided stormwater pollution prevention plan inspections and monitoring as required. They also provided quantity surveys and control points for construction activities.

Contract No. R13PC20194

Specification No. 20-C0800

Tracy Facility Pavement Rehabilitation – Delta Division – Central Valley Project, California

Allright Construction, Inc., Kerman, CA

Work Performed	May	1.4%
	Time Elapsed	12.8%
	Work Completed	1.4%
Contractor Earnings	May	\$8,615.00
	Previous	\$0
	Total to Date	\$8,615.00

Area Office Project Management

Project Manager: Brian Shinmoto, TO-430

Office Engineering

Contract Administrator: John Zimmerman, MPCO-230

Notice to Proceed was issued on April 18, 2013.

Invoice 1 was received and forwarded the Denver finance office for processing.

Field Engineering

Construction Manager: Steve Holmes, MPCO-320

Construction Representative: Frank Medberry, MPCO-341

Number of Contract Employees: 0

Worked Performed:

The contractor has scheduled site work to begin in June 2013.

Regional

Contract No. R10PC20R42

Specification No. 20-C0746

Hydropower Facility Modifications - Stage 1 – Battle Creek Salmon and Steelhead Restoration Project, California

RTA Construction/Ray Toney JV, Redding, CA

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	99.5%
Contractor Earnings:	May	\$0
	Previous	\$10,100,141.22
	Total to Date	\$10,100,141.22

Area Office Project Management

Project Manager: Mary Marshall, MP-203

Office Engineering

Contract Administrator: Kent Perkes, MPCO-225

No invoices were received this period.

The contractor has only to complete final submittals.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: John Pospishil, MPCO-321

Number of Contract Employees: 0

Work performed:

No onsite work was performed this period as all site work was completed in March 2013.

Substantial completion will be issued when as-built drawings are approved.

Contract No. R10PC20R80

Specification No. 20-C0759

Drought Relief – Construction of New Wells – ARRA Project No. 28.002 – California

Layne Christensen Company, Fontana, CA

Work Performed:	May	0%
	Time Elapsed	100%
	Work Completed	99.0%
Contractor Earnings:	May	\$424,641.96
	Previous	\$14,977,666.61
	Total to Date	\$15,402,308.57

Area Office Project Management

Project Manager: Kevin Clancy, MP-410

Office Engineering

Contract Administrator: John Zimmerman, MPCO-232

Invoice 14 was received and forwarded to the Denver finance office for processing. It was not for work done this period but was for work done through December 19, 2012.

The contractor has only to complete final submittals.

Field Engineering

Construction Manager: John E. Nelson, MPCO-328

Construction Representative: John E. Nelson, MPCO-328

Number of Contract Employees: 0

Work performed:

No site work was performed this period.

Contract No. R13PC20005

Specification No. 20-C0799

Baldwin Creek Fish Barrier – Battle Creek Salmon and Steelhead Restoration Project, California
Contractor Services Group, Inc.

Work Performed:	May	0%
	Time Elapsed	32.9%
	Work Completed	10.5%

Contractor Earnings:	May	\$0
	Previous	\$377,833.47
	Total to Date	\$377,833.47

Area Office Project Management

Project Manager: Mary Marshall, MP-203

Office Engineering

Contract Administrator: Kent Perkes, MPCO-225

No invoices were received this period.

Field Engineering

Construction Manager: Randy Wyatt, MPCO-305

Construction Representative: John Pospishil, MPCO-321

Number of Contract Employees: 0

Work performed:

No onsite work was performed this period. The contractor is waiting for the Federal Energy Regulatory Commission approval to perform site work.

Purchase Order No. R13PX20026

Specification No. 20-C0806

Pixley National Wildlife Refuge Alfalfa Valve Modifications – California

CW Crosser Construction, Inc., Anaheim, CA

Work Performed:	May	100%
	Time Elapsed	75.6%
	Work Completed	0%
Contractor Earnings:	May	\$0
	Previous	\$0
	Total to Date	\$0

Area Office Project Management

Project Manager: Kevin Clancy, MP-410

Office Engineering

Contract Administrator: John Zimmerman, MPCO-232

No invoices were received this period.

Field Engineering

Construction Manager: John E. Nelson, MPCO-328

Construction Representative: John E. Nelson, MPCO-328

Number of Contract Employees: 4

Work performed:

The contractor completed the placement of lean concrete, began and completed the placement of structural concrete and riprap, and completed all site work on May 9, 2013, the date of substantial completion.



Pixley National Wildlife Refuge Alfalfa Valve Modifications
Photograph of completed site work

Contracts in Warranty Status

R09PC20R03 20-C0677 Transformer K1A and K2A Replacements, Folsom Power Plant

There was no Office Engineering Administrative activity this period.

5-year warranty for K1A extends to January 30, 2016, and that for K2A extends to January 4, 2017.

R10PC20128 20-C0706 New Melones Power Plant Excitation System Replacement

There was no Office Engineering Administrative activity this period.

1-year warranty extended to May 24, 2013.

R10PC20R11 20-C0730 Red Bluff Pumping Plant and Fish Screen, Pumps and Motors

There was no Office Engineering Administrative activity this period.

3-year warranty extends to May 24, 2015.

R10PX20R45 20-C0750 Drought Relief, Well Enhancements

There was no Office Engineering Administrative activity this period.

1-year warranty for Tulare Irrigation District Well 1.16 extended to May 13, 2013. The 1-year warranties for all other wells have expired.

R10PX20R54 20-C0750 Drought Relief, Well Enhancements

There was no Office Engineering Administrative activity this period.

1-year warranty extends to December 6, 2013.

R10PC20R33 20-C0752 Red Bluff Pumping Plant and Fish Screen

Closeout submittals were dealt with this period.

1-year warranty extends to September 26, 2013.

R10PC20197 20-C0768 Control, Upgrade and Modernization of the Gantry and Bridge Cranes at the Folsom Dam and Powerplant

There was no Office Engineering Administrative activity this period.

2-year warranty extends to September 7, 2013.

R10PC20196 20-C0769 Control Upgrade and Modernization of the Gantry Crane at Nimbus Powerplant

There was no Office Engineering Administrative activity this period.

2-year warranty extends to June 13, 2013.

R12PC20055 20-C0776b Delta Cross Channel Gate Hoist Wire Rope Replacement

There was no Office Engineering Administrative activity this period.

1-year warranty extended to May 11, 2013.

R11PC20158 20-C0777 Stampede Powerplant and Switchyard Recoatings

There was no Office Engineering Administrative activity this period.

1-year warranty extends to August 12, 2013.

R11PC20124 20-C0780 Coleman National Fish Hatchery Barrier Weir Site Modifications

There was no Office Engineering Administrative activity this period.

1-year warranty extends to September 28, 2013.

R12PC20193 20-C0791 Shasta Dam Traffic Circle Pavement Rehabilitation

There was no Office Engineering Administrative activity this period.

1-year warranty extends to August 4, 2013.

R10PC20R32 20-C0749 Fish Screen Structure Phase 3, Contra Costa Canal

There was no Office Engineering Administrative activity this period.

1-year warranty for Siemens ultrasonic level transmitter ends August 21, 2013.
