BUREAU OF RECLAMATION

Boysen Reservoir Operations

Water Supply Forecasts and Reservoir Operations

Prepared November 2026


End of October Elevation and Storage: 4712.51 FT & 528,361 Acre-Feet


Actual Inflows (1,000 Acre-Feet):

Month	Inflow	Percent of Normal
October 25	39.5	69
November 25	42.4	85
December 25	39.5	99
January 26	35.4	94
February 26	36.2	96
March 26	45.4	85
April 26	44.1	84
May 26	62.0	44
June 26	98.5	34
July 26	46.4	37
August 26	32.7	66
September 26	45.0	97
October 26	63.0	112

Bureau of Reclamation
Missouri Basin Region
Wyoming Area Office
Mills, Wyoming

BOYSEN RESERVOIR

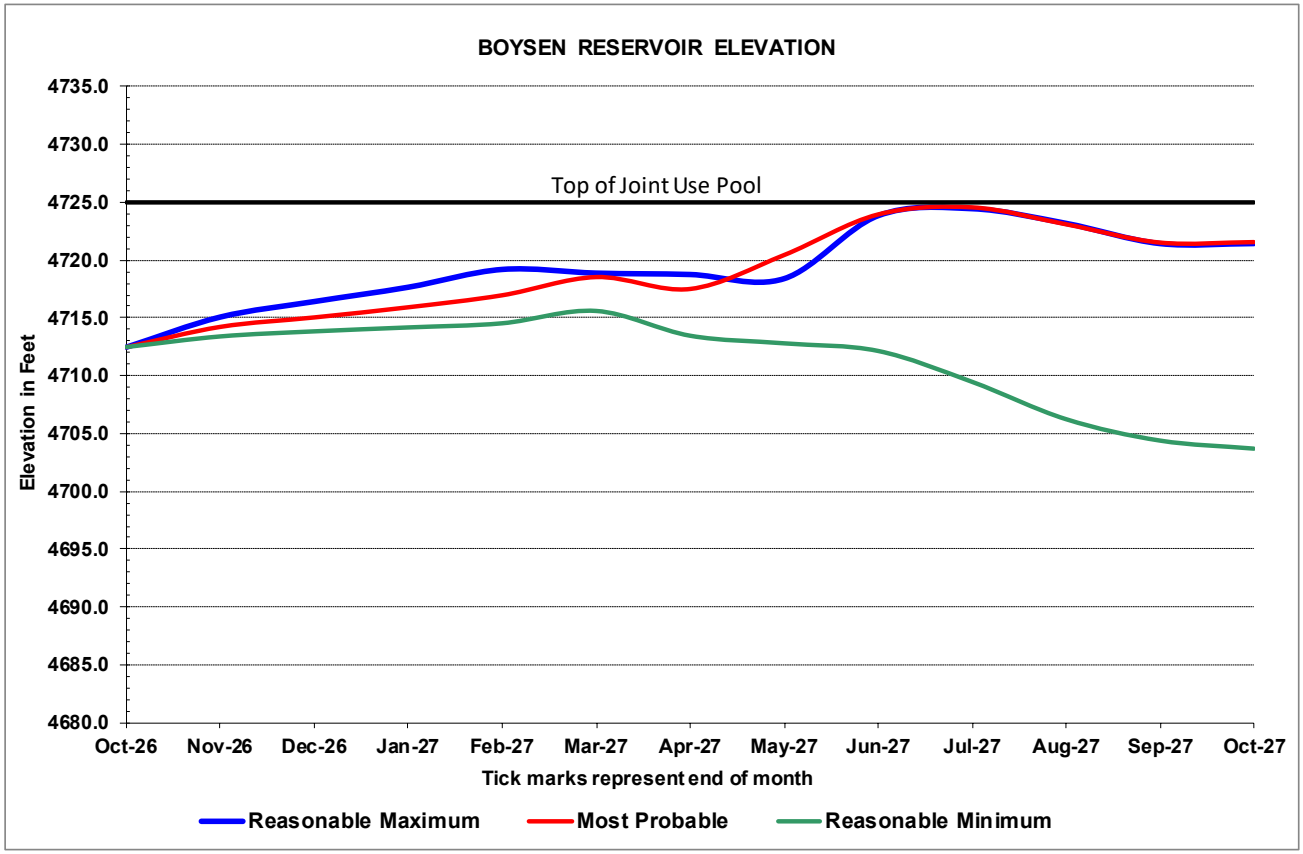

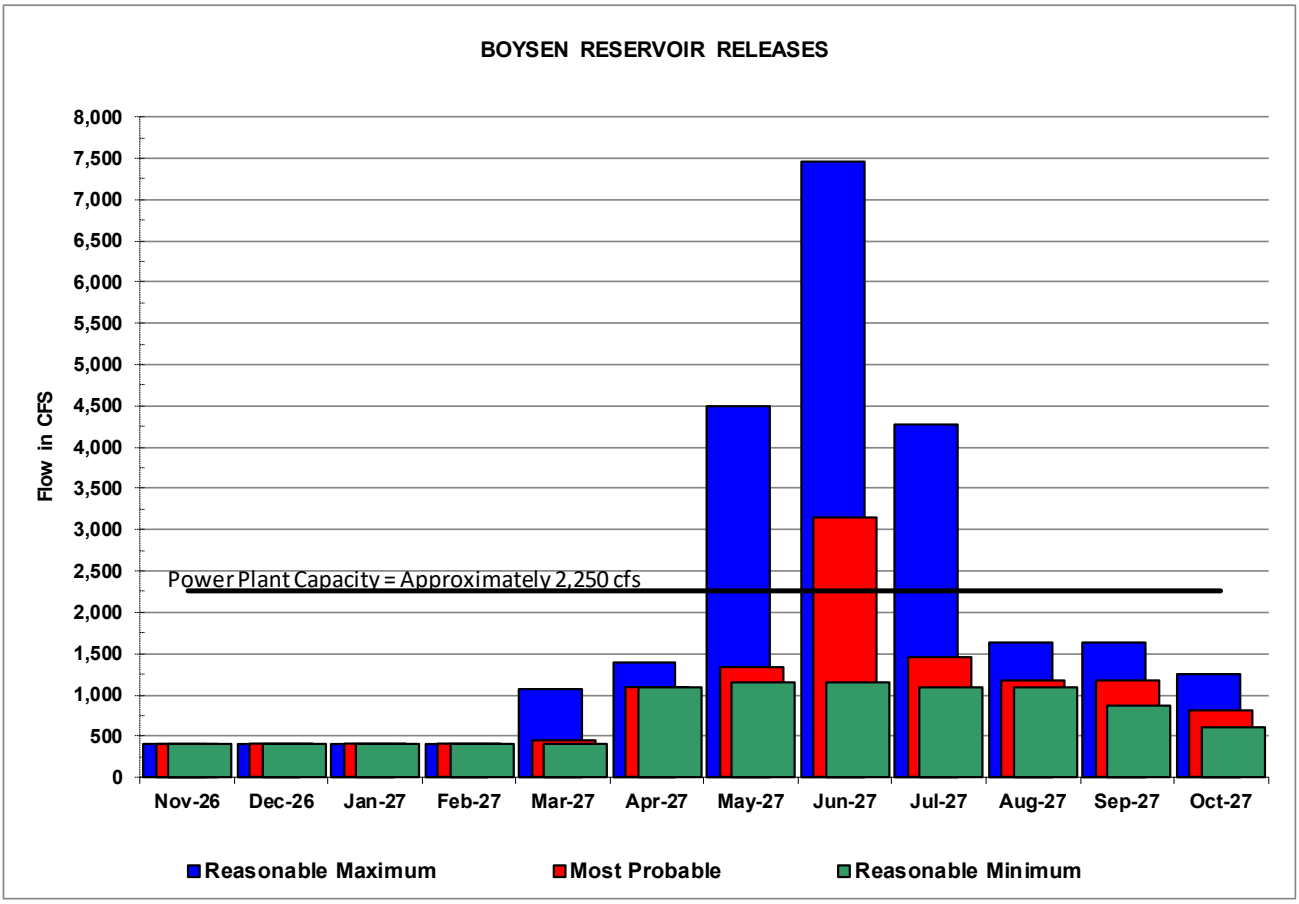

BOYAOP V1.48 Run: 02-Nov-2026 12:01
Based on Most Probable Inflows.

BOYSEN RESERVOIR MONTHLY OPERATIONS

Boysen Reservoir		Initial Cont	528.4 kaf	Maximum Cont	892.2 kaf	Minimum Cont	219.2 kaf					
		Elev	4712.51 ft	Elev	4732.20 ft	Elev	4685.00 ft					
2026		Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Total
Monthly Inflow	kaf	49.6	37.0	38.2	38.8	53.5	47.1	132.1	251.2	101.3	44.0	40.3	50.0	883.1
Monthly Inflow	cfs	834	602	621	699	870	792	2148	4222	1647	716	677	813	
Turbine Release	kaf	0.0	0.0	0.0	0.0	0.0	64.3	68.9	66.0	65.8	65.8	64.5	10.7	406.0
Bypass/Spill/Waste	kaf	23.8	24.6	24.6	22.2	27.5	0.0	13.1	120.9	23.6	6.0	4.9	38.5	329.7
Total Release	kaf	23.8	24.6	24.6	22.2	27.5	64.3	82.0	186.9	89.4	71.8	69.4	49.2	735.7
Total Release	cfs	400	400	400	400	447	1081	1334	3141	1454	1168	1166	800	
End-Month Content	kaf	554.2	566.6	580.2	596.8	622.8	605.6	655.7	720.0	731.9	704.1	675.0	675.8	
End-Month Elevation	ft	4714.25	4715.06	4715.93	4716.96	4718.52	4717.50	4720.41	4723.89	4724.50	4723.05	4721.48	4721.52	
Net Change Content	kaf	25.8	12.4	13.6	16.6	26.0	-17.2	50.1	64.3	11.9	-27.8	-29.1	0.8	147.4

Boysen Power Plant	2026	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Total
Turbine Release	kaf	0.0	0.0	0.0	0.0	0.0	64.3	68.9	66.0	65.8	65.8	64.5	10.7	406.0
Turbine Release	cfs	0	0	0	0	0	1081	1121	1109	1070	1070	1084	174	
Generation	gwh	0.000	0.000	0.000	0.000	0.000	5.522	5.949	5.758	5.952	5.954	5.757	0.954	35.846
Max Generation	gwh	0.000	0.000	0.000	0.000	0.000	5.760	5.952	5.760	5.952	5.952	5.760	0.952	36.088
% Max Generation	%	0	0	0	0	0	96	100	100	100	100	100	100	
Ave kwh/af							86	86	87	90	90	89	89	88
End-Month Power Cap	mw	16	16	16	16	16	16	16	16	16	16	16	16	

BOYAOP V1.48 Run: 02-Nov-2026 12:02
Based on reasonable MINIMUM inflows.

BOYSEN RESERVOIR MONTHLY OPERATIONS

Boysen Reservoir		Initial Cont	528.4 kaf	Maximum Cont	892.2 kaf	Minimum Cont	219.2 kaf					
		Elev	4712.51 ft	Elev	4732.20 ft	Elev	4685.00 ft					
2026		Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Total
Monthly Inflow	kaf	37.3	31.3	29.7	27.6	41.2	31.4	61.0	58.7	29.9	24.2	28.1	28.4	428.8
Monthly Inflow	cfs	627	509	483	497	670	528	992	986	486	394	472	462	
Turbine Release	kaf	0.0	0.0	0.0	0.0	0.0	64.3	70.7	68.4	67.6	67.0	51.2	10.9	400.1
Bypass/Spill/Waste	kaf	23.8	24.6	24.6	22.2	24.6	0.0	0.0	0.0	0.0	0.0	0.0	26.0	145.8
Total Release	kaf	23.8	24.6	24.6	22.2	24.6	64.3	70.7	68.4	67.6	67.0	51.2	36.9	545.9
Total Release	cfs	400	400	400	400	400	1081	1150	1150	1099	1090	860	600	
End-Month Content	kaf	541.9	548.6	553.7	559.1	575.7	542.8	533.1	523.4	485.7	442.9	419.8	411.3	
End-Month Elevation	ft	4713.43	4713.87	4714.21	4714.57	4715.64	4713.49	4712.83	4712.17	4709.49	4706.25	4704.39	4703.69	
Net Change Content	kaf	13.5	6.7	5.1	5.4	16.6	-32.9	-9.7	-9.7	-37.7	-42.8	-23.1	-8.5	-117.1

Boysen Power Plant	2026	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Total
Turbine Release	kaf	0.0	0.0	0.0	0.0	0.0	64.3	70.7	68.4	67.6	67.0	51.2	10.9	400.1
Turbine Release	cfs	0	0	0	0	0	1081	1150	1150	1099	1090	860	177	
Generation	gwh	0.000	0.000	0.000	0.000	0.000	5.341	5.783	5.558	5.406	5.139	3.800	0.800	31.827
Max Generation	gwh	0.000	0.000	0.000	0.000	0.000	5.760	5.952	5.760	5.952	5.952	5.760	0.952	36.088
% Max Generation	%	0	0	0	0	0	93	97	96	91	86	66	84	
Ave kwh/af							83	82	81	80	77	74	73	80
End-Month Power Cap	mw	16	16	16	16	16	16	16	15	15	14	13	13	

BOYAOP V1.48 Run: 02-Nov-2026 12:02
Based on Reasonable Maximum inflows.

BOYSEN RESERVOIR MONTHLY OPERATIONS

Boysen Reservoir		Initial Cont	528.4 kaf	Maximum Cont	892.2 kaf	Minimum Cont	219.2 kaf					
		Elev	4712.51 ft	Elev	4732.20 ft	Elev	4685.00 ft					
2026		Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Total
Monthly Inflow	kaf	63.0	45.7	44.9	48.3	60.7	81.3	270.6	541.9	274.6	76.3	65.0	77.6	1649.9
Monthly Inflow	cfs	1059	743	730	870	987	1366	4401	9107	4466	1241	1092	1262	
Turbine Release	kaf	0.0	0.0	0.0	0.0	41.2	66.9	71.4	68.5	67.5	66.1	64.9	10.8	457.3
Bypass/Spill/Waste	kaf	23.8	24.6	24.6	22.2	25.1	16.4	205.3	374.8	195.2	34.6	32.6	66.8	1046.0
Total Release	kaf	23.8	24.6	24.6	22.2	66.3	83.3	276.7	443.3	262.7	100.7	97.5	77.6	1503.3
Total Release	cfs	400	400	400	400	1078	1400	4500	7450	4272	1638	1639	1262	
End-Month Content	kaf	567.6	588.7	609.0	635.1	629.5	627.5	621.4	720.0	731.9	707.5	675.0	675.0	
End-Month Elevation	ft	4715.12	4716.46	4717.70	4719.24	4718.92	4718.80	4718.44	4723.89	4724.50	4723.23	4721.48	4721.48	
Net Change Content	kaf	39.2	21.1	20.3	26.1	-5.6	-2.0	-6.1	98.6	11.9	-24.4	-32.5	0.0	146.6

Boysen Power Plant	2026	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Total
Turbine Release	kaf	0.0	0.0	0.0	0.0	41.2	66.9	71.4	68.5	67.5	66.1	64.9	10.8	457.3
Turbine Release	cfs	0	0	0	0	670	1124	1161	1151	1098	1075	1091	176	
Generation	gwh	0.000	0.000	0.000	0.000	3.574	5.763	5.956	5.757	5.948	5.948	5.760	0.956	39.662
Max Generation	gwh	0.000	0.000	0.000	0.000	3.571	5.760	5.952	5.760	5.952	5.952	5.760	0.952	39.659
% Max Generation	%	0	0	0	0	100	100	100	100	100	100	100	100	
Ave kwh/af						87	86	83	84	88	90	89	89	87
End-Month Power Cap	mw	16	16	16	16	16	16	16	16	16	16	16	16	
